

2016 අංක 12 දරන තොරතුරු දැනගැනීමේ
අයිතිවාසිකම පිළිබඳ පනතේ 8වන වගන්තිය යටතේ
ප්‍රකාශයට පත් කළ යුතු අර්ථ වාර්ෂික වාර්තාව

2022.07.01 දින සිට 2022.12.31 දින දක්වා

ප්‍රවාහන හා මහාමාර්ග අමාත්‍යාංශය

10^a

2016 අංක 12 දරන තොරතුරු දැනගැනීමේ අයිතිවාසිකම පිළිබඳ පනතේ 8 වන වගන්තිය යටතේ
ප්‍රකාශයට පත් කළ යුතු අර්ධ වාර්ෂික වාර්තා - 2022.07.01 දින සිට 2022.12.31 දින දක්වා

අමාත්‍යාංශය - ප්‍රවාහන හා මහාමාර්ග අමාත්‍යාංශය

අමාත්‍ය - බන්දුල ගුණවර්ධන මැතිතුමා

මහාමාර්ග රාජ්‍ය අමාත්‍ය - සිරිපාල ගම්ලත් මැතිතුමා

ලේකම් - ආර්.චිං.ආර්. ජේ.මේයිර මහතා

පෙර මහාමාර්ග අමාත්‍යාංශය ලෙස පැවති මෙම අමාත්‍යාංශය 2022 ජූනි මස 26 වැනි දින නිකුත් කරන
ලද අංක 2281/31 දරන අති විශේෂ ගැසට් පත්‍රය මහින් ප්‍රවාහන හා මහාමාර්ග අමාත්‍යාංශය වශයෙන් නව
අමාත්‍යාංශයක් ලෙස ස්ථාපිත කරන ලදී.

තොරතුරු දැනගැනීමේ පනත අනුව ප්‍රවාහන හා මහාමාර්ග අමාත්‍යාංශය විසින් ප්‍රකාශයට පත් කළ යුතු
2022.07.01 - 2022.12.31 වන දින දක්වා වන අර්ධ වාර්ෂික වාර්තාවේහි මහාමාර්ග අංශය සඳහා වන
අර්ධ වාර්ෂික වාර්තාව මෙසේ ප්‍රකාශයට පත් කරන අතර ප්‍රවාහන අංශය උක්ත කාලය සම්බන්ධයෙන්
වන අර්ධ වාර්ෂික වාර්තාව එම අංශයේ තොරතුරු නිලධාරියා විසින් ප්‍රකාශයට පත් කරනු ඇත.

ලිපිනය: මහනැගුම මහමුදුර, 08වන මහල, බෙන්සිල් කොට්ඨාස මාවත, කොස්ටල්, බත්තරමුල්ල
දුරකථන අංක : 011 2050522 / 011 2887677
විද්‍යුත් තැපෑල : hwyadmin@mohsl.gov.lk
වෙබ් අඩවිය : www.mohsl.gov.lk

01. අමාත්‍යාංශයේ සංවිධාන සටහන - මහාමාර්ග අංශය ඇමුණුම 01 මහින් හා ග්‍රාමීය මාර්ග සංවර්ධන අංශය ඇමුණුම 02 මහින් ඉදිරිපත් කෙරේ.

02. අමාත්‍යාංශය තුළ ස්ථාපිත අංශ හා එහි කාර්යභාරය

අංශය	කාර්යභාරයන්	බලතළ	අනුගමනය කරනු ලබන රීති, නියෝග හා උපදේශ
පාලන අංශය	<ul style="list-style-type: none"> අමාත්‍යාංශයේ යටිතල පහසුකම් කාර්යක්ෂමව හා සංශීල්දායී ආකාරයට සැපයීම, ගොඩනැගිලි, යන්ත්‍ර සූත්‍ර හා නඩත්තු සම්බන්ධයෙන් අදාළ ආයතනයන්ගෙන් සේවා ලබා ගැනීම හා පවත්වාගෙන යුම. දෙදිනිකව අමාත්‍යාංශය වෙත ලැබෙන හා බැහැර යැවෙන ලිපි සම්බන්ධයෙන් කටයුතු කිරීම හා එහි සාධනීය බව සහතික කිරීම. අමාත්‍යාංශයේ ආරක්ෂක කටයුතු සහ පවත්තා කටයුතු නිසි පරිදි පවත්වාගෙන යාම. අමාත්‍යාංශ නිලධාරීන්ගේ රාජකාරී දුරකතන බිඳීපත් පියවීම. අමාත්‍යාංශ නිලධාරීන්ගේ සහ මාර්ග සංවර්ධන අධිකාරීයෙන් අනුයුත්ත කර ඇති නිලධාරීන්ගේ පෞද්ගලික ලිපිගොනු නඩත්තු කිරීම. අමාත්‍යාංශ කටයුතු සඳහා අවශ්‍ය ප්‍රවාහන පහසුකම් සැපයීම. අමාත්‍යාංශයේ සියලු වාහන ලියාපදිංචි කිරීම, නඩත්තු කිරීම, රක්ෂණය කිරීම, ආදායම බලපත්‍ර ලබා ගැනීම හා සියලු සංවිත වාහන සඳහා ඉන්ධන සැපයීම. වාහන අනතුරු සම්බන්ධයෙන් පියවර ගැනීම හා අදාළ අනතුර සඳහා රක්ෂණ වන්දි නිසි පරිදි ලබා ගැනීම. අමාත්‍යාංශ නිලධාරීන්ගේ සහ මාර්ග සංවර්ධන අධිකාරීයේ නිලධාරීන්ගේ විදේශ සංවාර සම්බන්ධ විදේශ ගමන් බලපත්‍ර, විසා, ගමන් වියදම හා දිමනා ලබා දීම පිළිබඳ කටයුතු හා දිවයිනෙන් බැහැර යාම සඳහා අවසර ගැනීමේ කටයුතු ඉටු කිරීම. 	<ul style="list-style-type: none"> ආයතන සංග්‍රහය මුදල් රෙගුලාසි රාජා සේවා කොමිෂන් සහා කාර්යය පරිපාලක රීති රාජා පරිපාලන වතුලේඛ ඡනාධිපති වතුලේඛ මුදල් අමාත්‍යාංශවතුලේඛ විශාම වැටුප් වතුලේඛ ප්‍රසම්පාදන මාර්ගෝපදේශ සංග්‍රහය අනි විශේෂ ගැසට පත්‍ර 2016 අංක 12 දරන තොරතුරු දැනගැනීමේ අයිතිවාසිකම පිළිබඳ පනත <p>උක්ත අණපනාන් මහින් ලබා දුන් හා අහිනියෝගනය කළ බලතළ ප්‍රකාරව</p>	<ul style="list-style-type: none"> ආයතන සංග්‍රහය මුදල් රෙගුලාසි රාජා සේවා කොමිෂන් සහා කාර්යය පරිපාලක රීති රාජා පරිපාලන වතුලේඛ ඡනාධිපති වතුලේඛ මුදල් අමාත්‍යාංශවතුලේඛ විශාම වැටුප් වතුලේඛ ප්‍රසම්පාදන මාර්ගෝපදේශ සංග්‍රහය අනි විශේෂ ගැසට පත්‍ර 2016 අංක 12 දරන තොරතුරු දැනගැනීමේ අයිතිවාසිකම පිළිබඳ පනත <p>උක්ත අණපනාන් වලට අදාළ විධිවිධාන යටතේ</p>

- අමාත්‍යාංශ නිලධාරීන්ගේ නිවාඩු, අතිකාල හා ගමන් වියදම් සම්බන්ධයෙන් කටයුතු කිරීම.
- අමාත්‍යාංශ නිලධාරීන් සඳහා ආපදා තෝරා, දේපල තෝරා, යනුරුපැදි තෝරා, උත්සව අත්තිකාරම ලබා දීම සම්බන්ධ කටයුතු සහ අගුහාර රක්ෂණ ඉල්ලම් කිරීම සම්බන්ධ කටයුතු කිරීම.
- අමාත්‍යාංශය මගින් ඉදිරිපත් කරනු ලබන අමාත්‍ය මැණ්ඩල සංදේශ, අමාත්‍ය මැණ්ඩලය වෙත යොමු කිරීම හා තීරණ අදාළ පාර්ශව වෙත දැන්වීම.
- පාර්ලිමේන්තු ප්‍රශ්න, උපදේශක කාරක සභා යෝජනා, මහජන පෙන්සම්, මානව හිමිකම කඩවීම හා ජනාධිපති කාර්යාලය හා විවිධ පාර්ශවයන්ගෙන් ලැබෙන පැමිණිලි, යෝජනා හා ඉල්ලම් සඳහා සුදුසු පියවර ගැනීම.
- 2016 අංක 12 දරන තොරතුරු පනත ත්‍රියාත්මක කිරීම.
- ගරුඅමාත්‍යතුමා, නියෝජ්‍යඅමාත්‍යතුමා, ලේකම සහ අමාත්‍යාංශ මාණ්ඩලික නිලධාරීන්ගේ රාජකාරී ගමන් වලදී නවාතැන් පහසුකම් වෙන් කිරීම සහ බිල්පත් නිරවුල් කිරීම.
- අනු දුම්රිය ප්‍රවේශපත් සහ දුම්රිය ගමන් බලපත්‍ර නිකුත් කිරීම.
- මාණ්ඩලික නිලධාරීන් සඳහා අත්තිකාරම ලබා දීම, අත්තිකාරම පියවීම, ලේඛනගත කිරීම හා ලේඛන යාචනකාලීන කර පවත්වාගෙන යාම, සුළු නැඩත්තු කටයුතු සහ විවිධ සුළු මුදල් ගෙවීම සම්බන්ධ සුළු මුදල් අග්‍රීම ලබා ගැනීම හා පියවීම.
- කණීජ්‍ය කාරය මාණ්ඩලය සඳහා නිල ඇඳුම් දීමනා අනුමත කිරීම, හාඡා පරිවර්තන වෙනුවෙන් ගෙවීම නිරවුල් කිරීම, ගෙවල් කුලී දීමනා අනුමත කිරීම, අමාත්‍යාංශ නිලධාරීන්ගේ සංග්‍රහ වියදම්, විවිධ වියදම් ප්‍රතිපූරණය කිරීම හා වියදම් නිරවුල් කිරීම.

	<ul style="list-style-type: none"> ජනාධිපතිවරණය, මහමැතිවරණය, පළාත් සහ මැතිවරණය හා පළාත් පාලන මැතිවරණ ඇතුළ ජන්ද විමසීම වලට අදාළ මැතිවරණ වකුලේබ අදාළ පාරිභව වෙත දැනුම දීම, එම මැතිවරණ වලට අදාළ ව තැපැල් ජන්දය දීම සම්බන්ධිකරණය සහ මැතිවරණ රාජකාරී සඳහා නිලධාරීන් පත්කිරීමේ කටයුතු සහ මැතිවරණ රාජකාරී වෙනුවෙන් ගෙවීම නිරවුල් කිරීමේ කටයුතු. පාලන අංශයේ ඉන්වෙන්ට්‍රේ ලේඛන පවත්වාගෙන යාම සහ අංශයට අදාළ ලිපිද්‍රව්‍ය ඉල්ලුම කිරීම, හාර ගැනීම හා බෙදා හැරීම. රාජ්‍ය පරිපාලන අමාත්‍යාංශය, මුදල් හා කුම සම්පාදන අමාත්‍යාංශය ඇතුළ අනෙකුත් රජයේ ආයතන වලින් ලැබෙන වකුලේබ හා නියෝග වෙන් වෙන් වශයෙන් ගොනු කිරීම හා යාචන්කාලීන කර පවත්වාගෙන යාම. සිංහල - ඉංග්‍රීසි සහ ඉංග්‍රීසි - සිංහල හාඡා පරිවර්තන කටයුතු. අමාත්‍යාංශ යටතේ ඇති මාර්ග සංවර්ධන අධිකාරීයේ ව්‍යාපෘති වල නව පත්කිරීම, සේවා දීර්ඝ කිරීම, නිවාඩු අනුමත කිරීම ඇතුළ ආයතනික කටයුතු. 		
ගිණුම අංශය	<ul style="list-style-type: none"> අමාත්‍යාංශය වෙත වාර්ෂික අයවැය මගින් වෙන් කරනු ලබන ප්‍රතිපාදන හැසිරවීම, මෙහෙයුවීම හා පාලනය කිරීම. ගිණුම අමාත්‍යාංශය සඳහා කාර්යක්ෂම සහ එලඟයී මූල්‍ය කළමනාකරණ පද්ධතියක් ක්‍රියාත්මක කිරීම. අමාත්‍යාංශය යටතේ පාලනය වන මාර්ග සංවර්ධන අධිකාරිය හා රාජ්‍ය හාණේධාරය අතර සම්බන්ධිකරණ කාර්යයයේ නියැලෙමින් ව්‍යාපෘති සඳහා අයවැය අරමුදල් තුම්වත්ව උපයෝගනය කිරීම. 	<ul style="list-style-type: none"> 2018 අංක 19 දරන විගණන පනත 2021 අංක 30 දරණ විසර්ථන පනත මුදල් රෙගුලාසි ප්‍රසම්පාදන මාර්ගෝපදේශ සංග්‍රහය ප්‍රසම්පාදන අත්පොත මුදල් අමාත්‍යාංශයේ වකුලේබ ආයතන සංග්‍රහය රාජ්‍ය පරිපාලන වකුලේබ 	<ul style="list-style-type: none"> 2018 අංක 19 දරන විගණන පනත 2021 අංක 30 දරන විසර්ථන පනත මුදල් රෙගුලාසි ප්‍රසම්පාදන මාර්ගෝපදේශ සංග්‍රහය ප්‍රසම්පාදන අත්පොත මුදල් අමාත්‍යාංශයේ වකුලේබ ආයතන සංග්‍රහය රාජ්‍ය පරිපාලන වකුලේබ

	<ul style="list-style-type: none"> ලපයේෂීත අරමුදල් තුළින් මූල්‍යමය කාර්යසාධනයන් රේට සමගාමීව සිදුකරනු ලබන වැයබරත් නිරික්ෂණය කර ගිණුම් අංශයේ මූල්‍යමය තන්ත්වය පිළිබඳ වාර්තා කිරීම . 	<p>උක්ත අණපනක් මගින් ලබා දුන් හා අභිනියෝගනය කළ බලකළ ප්‍රකාරව</p>	<p>උක්ත අණපනක් වලට අදාළ විධිවිධාන යටතේ</p>
අභ්‍යන්තර විගණන අංශය	<p>අමාත්‍යාංශය සඳහා වාර්ෂික ඇයේතමෙන්තු මගින් වෙන් කරන ලද ප්‍රතිපාදන තුළින් සිදු කෙරෙන මුදල් හා පරිපාලන කටයුතු පිළිබඳ අභ්‍යන්තර පාලනයට සහභාගී අදාළ ප්‍රතිපාදන මුදල් රෙගුලාසි හා අදාළ වකුලේබ උපදෙස් ප්‍රකාරව උපයෝගනය කර ඇති බව තහවුරු කිරීම හා එසේ මුදල් පරිහරණයනු ල ඇතිවන වැරදි හා වංචා වැළැක්වීම හා අනාවරණය කර ගැනීමට අදාළව,</p> <ul style="list-style-type: none"> මූල්‍ය ගනුදෙනු සම්බන්ධයෙන් සිදු විය හැකි වැරදි හා වංචා මගහරවා ගැනීමට අවශ්‍ය අභ්‍යන්තර සේදියි හා පාලන ක්‍රමයන් හඳුන්වා දීම. ගිණුම් හා වෙනත් වාර්තාවන්හි විශ්වාසනීයත්වය තහවුරු වන අයුරින් නිවැරදි මූල්‍යප්‍රකාශනයන් සකස් කිරීම සඳහා පවතින ගිණුම් පිළිවෙන් පිළිබඳ සමාලෝචනයන් සිදු කිරීම. වත්කම් පුරක්ෂිතව තබා ගැනීම හා ඒවා ආරක්ෂා කර ගැනීම සඳහා සුදුසු පියවරයන් ගෙන ඇති බවට තහවුරු කිරීම. රජය මගින් නිකුත් කරනු ලබන වකුලේබ හා උපදෙස් ප්‍රකාරව එකී නීති රාමු තුළ විධිමත් හා සාර්ථක අභ්‍යන්තර පාලනයක් සිදුවන්නේ දැයි සොයා බැලීම. අමාත්‍යාංශය යටතේ පවතින විදේශාධාර ව්‍යාපෘති වල ප්‍රගතිය යෝජිත සැලසුම් හා අනුකූල වන බව බව තහවුරු කිරීම හා අවශ්‍ය අවස්ථා වලදී විශේෂ විමර්ශන සිදු කිරීම තුළින් ඇති විය හැකි දුරවලනා අවම කිරීමට කටයුතු කිරීම. 	<ul style="list-style-type: none"> 2018 අංක 19 දරන විගණන පනත මුදල් රෙගුලාසි ආයතන සංග්‍රහය කළමනාකරණ විගණන දෙපාර්තමේන්තුවේ DMA/01/2019 දරන වකුලේබය <p>උක්ත අණපනක් මගින් ලබා දුන් හා අභිනියෝගනය කළ බලකළ ප්‍රකාරව</p>	<ul style="list-style-type: none"> 2018 අංක 19 දරන විගණන පනත මුදල් රෙගුලාසි ආයතන සංග්‍රහය කළමනාකරණ විගණන දෙපාර්තමේන්තුවේ DMA/01/2019 දරන වකුලේබය <p>උක්ත අණපනක් වලට අදාළ විධිවිධාන යටතේ</p>

<p>මෙම අංශය හාරයන් ඉඩම් අංශය හා ග්‍රාමීය මාර්ග සංවර්ධන අංශය ලෙස මූලික කොටස් දෙකකට බෙදා දැක්වීය හැක.</p> <p>ඉඩම් අංශය -</p> <ul style="list-style-type: none"> නාව ව්‍යාපෘති ඉදිකිරීමේදී හා ප්‍රතුරුත්ථාපනය කිරීමේදී අවශ්‍ය වන ඉඩම් අත්කර ගැනීමේ හා ප්‍රතිස්ථානගත කිරීමේ විශේෂ කමිටුවක් පැවැත්වීම. මහජන දුක් ගැනවිලි විසඳීමට සහාය වීම. ඡනාධිපති ලේකම් කාර්යාලය, පාර්ලිමේන්තු කාරකා සහා, මිමුඩිස්මන් කාර්යාලය වැනි ආයතන වලට තොරතුරු ලබා දීම සහ එම ආයතන සමඟ මත්‍ය සම්බන්ධිකරණයක් පවත්වාගෙන යාම. අදාළ ව්‍යාපෘතිය, ඉඩම් අමාත්‍යාංශය, රජයේ මූල්‍යාලය, තක්සේරු දෙපාර්තමේන්තුව, ජ්‍රාදේශීය ලේකම් කාර්යාල වැනි ව්‍යාපෘති වලට අදාළ ආයතන සමඟ මත්‍ය සම්බන්ධිකරණය් පවත්වා ගෙන යාම. <p>ව්‍යාපෘති</p> <p>මගනැගුම් අංශය -</p> <ul style="list-style-type: none"> ව්‍යාපෘතිය වූ ග්‍රාමීය ප්‍රවීග මාර්ග පද්ධතියක් ඇති කිරීමටත්, ආර්ථික හා සාමාජික සංවර්ධනයටත් මත්‍ය පිවුවහලක් වෙමින් ග්‍රාමීය මාර්ග සංවර්ධන ව්‍යාපෘති ත්‍රියාත්මක කරනු ලබන අතර ග්‍රාමීය මාර්ග සංවර්ධනය සඳහා ආයෝජන ඉහළ නාවමින් වඩාත් ගක්තිමත් මාර්ග ජාලයක් ඉදි කිරීම ක්‍රිඩ්‍රිත් ග්‍රාමීය ප්‍රජාවගේ සමාජ ආර්ථික සංවර්ධනය සඳහා ආයකත්වයක් සැපයීම. වාර්ෂික වැඩ සැලැස්ම හා වකුලේල්බ සකස් කිරීම. අදාළ සැලැස්ම හා වකුලේල්බ අනුව ග්‍රාමීය මාර්ග සංවර්ධනය සඳහා යෝජනා කැඳවීම. සංවර්ධනය කිරීම සඳහා අවශ්‍ය නිරදේශ ලබා ගැනීම හා ඇස්කමෙන්තු සකස් කිරීම.

	<ul style="list-style-type: none"> ක්‍රියාත්මක ආයතන වෙත ප්‍රමාණවත් ප්‍රතිපාදන නිදහස් කිරීම හා උපදෙස් ලබා දීම. ප්‍රාදේශීය මට්ටම්වල සම්ති හා එහි ක්‍රියාකාරී නිලධාරීන් දැනුවත් කිරීමේ වැඩසටහන් පැවැත්වීම. ක්ෂේත්‍ර පරික්ෂණ / නිරීක්ෂණ පැවැත්වීම. 	<p>උක්ත අණපනක් මගින් ලබා දුන් හා අභිනියෝගනය කළ බලකළ ප්‍රකාරව</p>	<p>උක්ත අණපනක් වලට අදාළ විධිවිධාන යටතේ</p>
සැලසුම් හා මෙහෙයුම් අංශය	<ul style="list-style-type: none"> ව්‍යාපෘති සඳහා සම්බන්ධවන සියලු පාර්ශවයන්ගේ උපදෙස් අනුව මහාමාරුග අංශයේ ප්‍රතිපත්ති සකස් කිරීම. මහාමාරුග අංශයේ ව්‍යාපෘති සඳහා සැලසුම් සකස් කිරීම, ක්‍රියාත්මක කිරීම හා අධික්ෂණය කිරීම. රජයේ ප්‍රමුඛතා හා අයවැය ප්‍රතිපාදන අනුව වාර්ෂික කාර්යසාධන ක්‍රියාවලිය සකස් කිරීම. වාර්ෂික අයවැය යාකච්ඡා සඳහා වාර්ෂික කාර්යය සාධන වාර්තා හා ප්‍රගති වාර්තා සැකසීම. මහාමාරුග අංශයට අදාළ දත්ත රස් කිරීම හා විව්ලනයන්ට අනුව යාවත්කාලීන කර දත්ත පද්ධතියක් සැකසීම. අමාත්‍යාංශයට අනුබද්ධිත ප්‍රමුඛ ව්‍යාපෘති සඳහා ව්‍යාපෘති සම්බන්ධිකරණ කමිටු රස්වීම පැවැත්වීම හා සම්බන්ධිකරණය කිරීම. රජයේ මූල්‍යාධාර ලබා ගැනීම සඳහා ඉදිරිපත් කරන ලද ව්‍යාපෘති වාර්තා විශ්ලේෂණය කර එම ව්‍යාපෘති වාර්තාවලට අදාළ සංකල්ප වාර්තා අදාළ අනුමැතිය සඳහා ජාතික ක්‍රමසම්පාදන දෙපාර්තමේන්තුව හා විදේශ සම්පත් දෙපාර්තමේන්තුව වෙත ඉදිරිපත් කිරීම. 	<ul style="list-style-type: none"> මුදල් අමාත්‍යාංශයේ ව්‍යුත්ලේඛ ආයතන සංග්‍රහය රාජ්‍ය පරිපාලන ව්‍යුත්ලේඛ 2016 අංක 12 දරන තොරතුරු දැනගැනීමේ අධිනිවාසිකම පිළිබඳ පනත <p>උක්ත අණපනක් මගින් ලබා දුන් හා අභිනියෝගනය කළ බලකළ ප්‍රකාරව</p>	<ul style="list-style-type: none"> මුදල් අමාත්‍යාංශයේ ව්‍යුත්ලේඛ ආයතන සංග්‍රහය රාජ්‍ය පරිපාලන ව්‍යුත්ලේඛ 2016 අංක 12 දරන තොරතුරු දැනගැනීමේ අධිනිවාසිකම පිළිබඳ පනත <p>උක්ත අණපනක් වලට අදාළ විධිවිධාන යටතේ</p>

	<ul style="list-style-type: none"> • විවිධ ජාත්‍යන්තර ආධාර ලබා දෙන සංවිධානයන් මහින් ඉදිරිපත් කරනු ලබන රාජකාරී ලිපි ලේඛන සඳහා අමාත්‍යාංශ ලේකම් නියෝජනය කරමින් අදහස් දැක්වීම, පුනරීක්ෂණය කිරීම, රස්වීම සඳහා සහභාගී වීම, සටහන් තැබීම හා එකඟතාවයන්ට එළඟීම. • අමාත්‍යාංශයේ ඉලක්ක, අරමුණු, ත්‍රියාවලින්, සංවර්ධන ප්‍රමුඛතාවයන් අනුව විවිධ අධිකාරීන් මහින් මෙහෙයවන රස්වීම, වැඩමුළ හා සම්මත්තුණ සඳහා සහභාගී වීම. 	
--	--	--

ප්‍රසම්පාදන අංශය	<ul style="list-style-type: none"> මාර්ග සංවර්ධන අධිකාරිය යටතේ පවතින ව්‍යාපෘති මගින් සකස් කර මෙම අංශය වෙත යොමු කරන වාර්ෂික ප්‍රසම්පාදන සැලපුම්බි සියලු දත්ත යම්බන්ධිකරණ කටයුතු සිදු කිරීම මගින් වාර්ෂික ප්‍රසම්පාදන සැලස්ම පිළියෙළ කිරීම. එසේ පිළියෙළ කරනු ලබන සමස්ත වාර්ෂික ප්‍රසම්පාදන සැලස්ම මූදල් අමාත්‍යාංශයේ රාජ්‍ය මූදල් දෙපාර්තමේන්තුව වෙත යොමු කිරීමට කටයුතු කිරීම සහ අවශ්‍ය අවස්ථා වලදී වෙනත් රේඛීය අමාත්‍යාංශ, ජාතික ප්‍රසම්පාදන කොමිෂන් සභාව, ප්‍රසම්පාදන අභියාචනා මණ්ඩලය වැනි ආයතන වෙත යොමු කිරීමට ද කටයුතු කිරීම. 	<ul style="list-style-type: none"> ප්‍රසම්පාදන මාර්ගෝපදේශ සංග්‍රහය 2006 හාණ්ඩ හා වැඩි ප්‍රසම්පාදන මාර්ගෝපදේශ සංග්‍රහය 2007 උපදේශන සේවා ප්‍රසම්පාදන අත්පොත හා ඒ සම්බන්ධව කාලීනව නිකුත් කරන ලද පරිපූරක ලියවිලි හාණ්ඩාගාරය විසින් කළින් කළට නිකුත් කරනු ලැබූ වනුලේබ මූල්‍ය රෙගලාසි ආයතන සංග්‍රහය 2016 අංක 12 දරන තොරතුරු දැනගැනීමේ අයිතිවාසිකම පිළිබඳ පනත <p>උක්ත අණපනක් මගින් ලබා දුන් හා අභිනියෝගනය කළ බලත්ල ප්‍රකාරව</p>	<ul style="list-style-type: none"> ප්‍රසම්පාදන මාර්ගෝපදේශ සංග්‍රහය 2006 හාණ්ඩ හා වැඩි ප්‍රසම්පාදන මාර්ගෝපදේශ සංග්‍රහය 2007 උපදේශන සේවා ප්‍රසම්පාදන අත්පොත හා ඒ සම්බන්ධව කාලීනව නිකුත් කරන ලද පරිපූරක ලියවිලි හාණ්ඩාගාරය විසින් කළින් කළට නිකුත් කරනු ලැබූ වනුලේබ මූල්‍ය රෙගලාසි ආයතන සංග්‍රහය 2016 අංක 12 දරන තොරතුරු දැනගැනීමේ අයිතිවාසිකම පිළිබඳ පනත <p>උක්ත අණපනක් වලට අභ්‍ය විවිධාන යටතේ</p>
---------------------	---	---	---

ඉංජිනේරු අංශය	<ul style="list-style-type: none"> මහාමාරග ඉදිකිරීම් සම්බන්ධව සියලු ඉංජිනේරු මය කටයුතු අධික්ෂණය කිරීම හා අදාළ කාක්ෂණික විගණනයන් සිදු කිරීම. දේශීය හා විදේශීය අරමුදල් යටතේ ක්‍රියාත්මක වන ව්‍යාපෘති වල ප්‍රගතිය හා තත්ත්වය අධික්ෂණය කිරීම. වාර්ෂික මාරුගත මිලගණන් ලේඛනය සැකසීම. මාරුග උත්සෙෂණගත කිරීම සිදු කිරීම. විවුමන් මිලදී ගැනීම වලදී ගැනුමකරුවන්ගේ අන්තර්ජාල තහවුරු කිරීම. සියලු ව්‍යාපෘති වලට අදාළ “ව්‍යාපෘති සම්බන්ධිකරණ කමිටු” සඳහා සහභාගී විම හා ඒවායේ සම්බන්ධිකරණ කටයුතු සිදු කිරීම. සියලු ව්‍යාපෘති වලට අදාළ කාර්යය සාධන වාර්තා පරික්ෂා කිරීම. අමාත්‍යාංශප්‍රසම්පාදන කමිටුවේ සහභාගීත්වය දැරීම. අමාත්‍යාංශ වෙබ් අඩවිය යටත්කාලීන කර පවත්වාගෙන යාම. 	<ul style="list-style-type: none"> ප්‍රසම්පාදන මාරුගෝපදේශ සංග්‍රහය 2006 හා එක්ව හා වැඩි 2008 අංක 40 දරණ ජාතික මංමාවත් පනත Highway Schedule of Rates (HSR) මූල්‍ය රෙගුලාසි 2018 අංක 19 දරන විගණන පනත ආයතන සංග්‍රහය මූල්‍ය රෙගුලාසි 2016 අංක 12 දරන තොරතුරු දැනගැනීමේ අයිතිවාසිකම පිළිබඳ පනත 	<ul style="list-style-type: none"> ප්‍රසම්පාදන මාරුගෝපදේශ සංග්‍රහය 2006 හා එක්ව හා වැඩි 2008 අංක 40 දරණ ජාතික මංමාවත් පනත Highway Schedule of Rates (HSR) මූල්‍ය රෙගුලාසි 2018 අංක 19 දරන විගණන පනත ආයතන සංග්‍රහය මූල්‍ය රෙගුලාසි 2016 අංක 12 දරන තොරතුරු දැනගැනීමේ අයිතිවාසිකම පිළිබඳ පනත
---------------	--	---	---

3. එක් එක් අංශ සඳහා වගකිව පුතු නිලධාරීන් (මහාමාරිග අංශය)

අංශය	නම	තනතුර	දුරකථන අංකය
පාලන අංශය	ශ්‍ර.එච්.සී.ප්‍රියන්ත මහතා (ශ්‍රීලං.ප.යේ) (විශේෂ)	අනිරේක ලේකම් (පාලන)	2862712/2862746
	ඩි.වි.ටි.පි. දයානන්ද මිය (ශ්‍රීලං..ප.යේ)	පොත්ත්ය සහකාර ලේකම් (පාලන)	2887473
	එන්.එස්.අනුකෝරල මිය (ශ්‍රීලං.ප.යේ)	අධ්‍යක්ෂ (ව්‍යාපෘති කළමනාකරණ)	2050518
	චඛ.එච්.එන් තරුග මහතා (ශ්‍රීලං.ප.යේ)	සහකාර ලේකම් (ව්‍යාපෘති කළමනාකරණ)	2887472
	එච.එම.චි.මධුජානි මිය (ශ්‍රීලං.ප.යේ)	සහකාර ලේකම් (පාලන)	2871039
	ඒ.එස්.කේ. අමරකොන් මෙය	නීති නිලධාරී	2862717
හිඹුම් අංශය	ඒ.කේ.එන්.එස්.පෙරේරා මහතා (ශ්‍රීලං.ග.යේ) (විශේෂ)	ප්‍රධාන මූල්‍ය නිලධාරී	2862765
	වි.ඒ.ඩී.සී.එන්.විරක්කොචි මිය (ශ්‍රීලං.ග.යේ)	ප්‍රධාන ගණකාධිකාරී	2862765
	එල්.ඒ.එස් ද්‍රූෂ්‍යන්ති මිය (ශ්‍රීලං..ග.යේ)	ගණකාධිකාරී (ව්‍යාපෘති)	2872292
	ඒ. පි. පි. මහේෂිකා මිය (ශ්‍රීලං.ග.යේ)	ගණකාධිකාරී (හිඹුම්)	2887465
	බි.එන්.එස්. පෙරේරා මිය (ශ්‍රී.ලං.ග.යේ)	ගණකාධිකාරී (ගෙවීම්)	2050513
අභ්‍යන්තර විගණන අංශය	ඩි.කේ.වි.සමන්මලී මිය (ශ්‍රීලං.ග.යේ)	ප්‍රධාන අභ්‍යන්තර විගණක	2050531
සංවර්ධන අංශය	එස්.ඒස්.එම.එච්.සී. සමරකොන් මිය (ශ්‍රී.ලං.ප.යේ. විශේෂ)	අනිරේක ලේකම් (සංවර්ධන)	2865310
	ඒ.ඒ. මධුසාඛ මහතා (ශ්‍රීලං.ප.යේ)	පොත්ත්ය සහකාර ලේකම් (සංවර්ධන)	2862686

ඉංඩිනෝරු අංශය	කේ.බ්.වී. ඉන්දපාල මහතා (ශ්‍රීලං.ඉ.සේ) (විශේෂ)	අතිරේක ලේකම (ඉංඩිනෝරු)	2868703
	ඩී. එම්. කේ. එස්. දියානායක මහතා (ශ්‍රීලං.ඉ.සේ)	අධ්‍යක්ෂ (ඉංඩිනෝරු)	2887463
	වයි.නී.පී. කහටගහවත්ත මෙය (ශ්‍රීලං.ඉ.සේ)	සහකාර අධ්‍යක්ෂ (ඉංඩිනෝරු)	2887543
	පී. පී. ජයසේකර මිය (ශ්‍රීලං.ඉ.සේ)	සහකාර අධ්‍යක්ෂ (ඉංඩිනෝරු)	
	චි. එම්. සී. එච්. මැණිකේ මහත්මිය (ශ්‍රීලං.ඉ.සේ)	සහකාර අධ්‍යක්ෂ (ඉංඩිනෝරු)	2887543
සැලසුම හා මෙහෙයුම අංශය	එස්.එස් මුදලිගේ මහතා (ශ්‍රීලං.තු.සේ) (විශේෂ)	අධ්‍යක්ෂ ජනරාල (සැලසුම)	2864726
	චඩ.එච්.කේ.බ්.බී. රත්නායක මහතා (ශ්‍රීලං.තු.සේ)	අධ්‍යක්ෂ (සැලසුම හා මෙහෙයුම)	2050581
	ප්‍රූජ්පානි අමරතුංග මිය (ශ්‍රීලං.තු.සේ)	නියෝජ්‍ය අධ්‍යක්ෂ (සැලසුම හා මෙහෙයුම)	2888011
	පී.පී. සේවාපනිරණ මිය (ශ්‍රීලං.තු.සේ)	නියෝජ්‍ය අධ්‍යක්ෂ (සැලසුම හා මෙහෙයුම)	2050583
ප්‍රසම්පාදන අංශය	ගාමිණී රත්නායක මහතා	ප්‍රසම්පාදන විශේෂඝ	2050597

3.1 එක් එක් අංශය සඳහා වගකිව පුතු නිලධාරීන් (ග්‍රාමීය මාරුග සංවර්ධන අංශය)

අංශය	නම	කනෑතුර	දුරකථන අංකය
පාලන අංශය	චි. රණවිර මහතා (ශ්‍රීලං.ප.සේ.) (විශේෂ)	අතිරේක ලේකම් (ග්‍රාමීය මාරුග සංවර්ධන)	2050535
ගිණුම අංශය	ඒ.ඒ.එස්.පි. විජේරත්න මහත්මිය (ශ්‍රීලං.ග.සේ)	ප්‍රධාන ගණකාධිකාරී	2887461
අභ්‍යන්තර විගණක අංශය	චි.ඒ.එච්.එල්. සෙනෙවිරත්න මෙය (ශ්‍රීලං.ග.සේ)	ප්‍රධාන අභ්‍යන්තර විගණක	2050555
සැලපුම අංශය	අයි.එම්.ඩී. ගුණරත්න මහත්මිය (ශ්‍රීලං.කු.සේ)	අධ්‍යක්ෂ (සැලපුම)	2865315
	එස්.එස්. ගොඩකන්ද ආරච්චිගේ මහතා (ශ්‍රීලං.කු.සේ)	නියෝජා අධ්‍යක්ෂ (සැලපුම)	2871099
ඉංජිනේරු අංශය	එස්.ඒ.කේ. පුබසිංහ මහත්මිය (ශ්‍රීලං.ඉ.සේ)	අධ්‍යක්ෂ ජනරාල් (ඉංජිනේරු)	2050557
	ඒ.එම්.ඩී.සී. බණ්ඩාර මහතා (ශ්‍රීලං.ඉ.සේ)	ඉංජිනේරු	2050523

4. අමාත්‍යාංශයේ බලකළ (මහාමාරුග අමාත්‍යාංශයට අදාළව)

(අ). 2008 අංක 40 දරන ජාතික මංත්‍රවත් පනත

(ආ). 1981 අංක 73 දරන මාරුග සංවර්ධන අධිකාරී පනත

5. අමාත්‍යාංශයේ කාර්යාලයෙහි හා කර්ත්වාලයෙහි

01. “සෞඛ්‍යාගායයේ දැක්ම “ප්‍රතිපත්ති ප්‍රකාශයට අනුකූලව සහ රුපය මගින් ක්‍රියාත්මකකරවු ලබන ජාතික ප්‍රතිපත්තින් මත පිහිටා ප්‍රවාහන හා මහාමාරුග විෂයයට සහ දෙපාර්තමේන්තු හා රාජ්‍ය සංස්ථාවන්හි විෂයයන්ට අදාළ ප්‍රතිපත්ති, වැඩසටහන් සහ ව්‍යාපෘති සම්පාදනය කිරීම, ක්‍රියාත්මක කිරීම, පසු විපරම කිරීම හා ඇගයිම

02. අමාත්‍යාංශ විෂය පරියට අයත්වන මහජන සේවාවන් කාර්යක්ෂමව හා මහජන හිතකාම් අයුරින් ලබා දීම

03. නාය්‍යාලු හා දුෂ්‍රණය පිටු දකිනීන් අමාත්‍යාංශයේ කාර්යභාරය ඉටු කිරීම සහතික කිරීමට ඉවහල් වන ආකාරයට නවීන කළමනාකරණ තුම් හා තාක්ෂණය යොදා ගනීමින් සියලුම තුම් සහ විධ ප්‍රතිසංස්කරණය කිරීම

04. ග්‍රාමීය, පුරුව නගර හා නාගරික ප්‍රදේශ සඛෙදනා පුළුල් කරමින් ජනතා කේත්තිය ආර්ථික හා සමාජ සංවර්ධනයක් ඇතිවන ලෙස උසස් තත්ත්වයෙන් යුත් ජාතික මහාමාරුග පද්ධතිය වැඩිදියුණු කිරීම සහ ප්‍රශන් ක්‍රියාත්මක පවත්වාගෙන යාම

05. අධිවේගී මාරුග සංවර්ධනය, නඩත්තුව, ගාස්තු නියම කිරීම, රස් කිරීම සහ නියාමනය කිරීම

06. පළාත් සහ පළාත් පාලන ආයතනවලට අයත් මාරුග පිළිබඳ ජාතික ප්‍රතිපත්ති පදනම් කොටගත් වැඩසටහන් හා ව්‍යාපෘති සකස් කිරීම, එම වැඩසටහන් සහ ව්‍යාපෘති සම්බන්ධිකරණය හා මෙහෙයුම්

07. වාහන තදබෑදය අවම කිරීම සඳහා වාහන අංශන පිහිටුවීම

08. ග්‍රාමීය මාරුග ජාලය සංවර්ධනය හා නවිකරණය කිරීම

09. ප්‍රධාන මාරුග සහ අධිවේගී මාරුග සඳහා ඉහළ මට්ටමේ ප්‍රවේශයක් සඳහා විකල්ප මාරුග පද්ධතියක් සකස් කිරීම

10. මහි තොටුපළ සේවාවන් සැකසීම

6. අමාත්‍යාංශය යටතේ වන ජොදු අධිකාරීන් පිළිබඳ විස්තර

ජොදු අධිකාරිය	බලනල	කාර්යයන් හා කර්තව්‍යන්
මාරුග සංවර්ධන අධිකාරිය සහ එහි පාලිත සමාගම (මාරුග සංවර්ධන අධිකාරීයේ අධ්‍යක්ෂ ජනරාල් ගේ අධික්ෂණය යටතේ ක්‍රියාත්මක වේ)	<ul style="list-style-type: none"> 1981 අංක 73 මාරුග සංවර්ධන අධිකාරී පනත 2008 අංක 40 ජාතික ම.මාවන් පනත 	<ul style="list-style-type: none"> ජාතික මහාමාරුග පද්ධතිය සතු මාරුග හා පාලම සංවර්ධනය කිරීම හා නඩත්තු කිරීම. පවතින මහාමාරුග පද්ධතිය වැඩි දියුණු කිරීමේ අරමුණින් නව මහාමාරුග, පාලම හා අධිවේශී මාරුග සැලසුම කිරීම, නිර්මාණය කිරීම හා ඉදි කිරීම. අනාගත ගමනාගමන හා ප්‍රවාහන ඉල්ලුම පුරෝකළනය කිරීම තුළින් අනාගත මාරුග පද්ධති සැලසුම කිරීම හා එකී ඉල්ලුම සපුරාලීම සඳහා අවශ්‍ය ව්‍යාපෘති යෝජනා සැකසීම. ගමනාගමනය හා ආරක්ෂාව පිළිබඳ සාමාජික අභිලාෂයන් තහවුරු කළ හැකි පරිදි මාරුග පද්ධතිය ඉදි කිරීම හා සංවර්ධනය කිරීම. සම්මත පිරිවිතරයන්ට අනුකූලව මාරුග පද්ධති ඉදි කිරීම හා නඩත්තු කිරීම තුළින් මහජනයාගේ ප්‍රවාහන අවශ්‍යතා වලට බාධාකාරී නොවන ආකාරයේ මාරුග පද්ධතියක් ඇති කිරීම. මහජන මුදල් වැය කරමින් ඉදි කරන මාරුග පද්ධති තුළින් ප්‍රමාණවත් ආරක්ෂා ප්‍රතිලාභ නැවත මහජනයා වෙතවම ලැබෙන බව තහවුරු කිරීම සඳහා අදාළ ව්‍යාපෘති වලට අදාළව ගෙයනා අධ්‍යාපන කටයුතු හිදු කිරීම හා අදාළ ව්‍යාපෘති පිළිබඳ පැන්වාත් අගය කිරීම සිදු කිරීම.
රාජ්‍ය සංවර්ධන හා නිර්මාණ නීතිගත සංස්ථාව		<ul style="list-style-type: none"> මාරුග, පාලම, ගොඩනැගිලි, ජල සම්පාදන ව්‍යාපෘති, වැව ප්‍රතිසංස්කරණය, පෙර සහ කොන්ක්‍රිට තිපැපුම හා ඉදිකිරීම අමුදව්‍ය නිෂ්පාදනය කිරීම

7. 2022 අමාත්‍යාංශයේ එක් එක් අංශ හා ව්‍යාපෘති සඳහා ප්‍රතිපාදන සහ වියදම (අමුණුම අංක 03 මහින් ඉදිරිපත් කෙරේ.)
8. 2022 වර්ෂය සඳහා අමාත්‍යාංශයේ ප්‍රසාද ප්‍රතිපාදන යැලැයේම (අමුණුම අංක 04 මහින් ඉදිරිපත් කෙරේ)
9. තොරතුරු ලබා ගැනීම සඳහා පුරවැසියන්ට ලබා ගත හැකි පහසුකම්
 - අමාත්‍යාංශ වෙබ් අඩවිය - www.mohsl.gov.lk
 - අමාත්‍යාංශ විද්‍යුත් තැපෑල - hwyadmin@mohsl.gov.lk
10. පන් කළ තොරතුරු නිලධාරී පිළිබඳ විස්තර (මහාමාරිග අංශයට අදාළව)
 - තොරතුරු නිලධාරී - එච්.එම්.එච්.මද්‍යානී


තනතුර	- සහකාර ලේකම් (පාලන)
දුරකථන අංක	- 0112863296
විද්‍යුත් තැපෑල	- tharanga1417@gmaill.com
 - තම් කළ නිලධාරී - ඩු.එච්.සී.ප්‍රියත්ත

තනතුර	- මහාමාරිග අමාත්‍යාංශයේ අනිරෝක ලේකම් (පාලන)
දුරකථන අංකය	- 0112862712 / 0112862746


6. අමාත්‍යාංශය යටතේ වන පොදු අධිකාරීන් පිළිබඳ විස්තර

පොදු අධිකාරිය	බලකළ	කාර්යයන් හා කර්තව්‍යයන්
මාරුග සංවර්ධන අධිකාරිය සහ එහි පාලිත සමාගම (මාරුග සංවර්ධන අධිකාරීයේ අධ්‍යක්ෂ ජනරාල් ගේ අධික්ෂණය යටතේ ත්‍රියාන්තමක වේ)	<ul style="list-style-type: none"> 1981 අංක 73 මාරුග සංවර්ධන අධිකාරී පනත 2008 අංක 40 ජාතික මංමාවන් පනත 	<ul style="list-style-type: none"> ජාතික මහාමාරුග පද්ධතිය සඳහා මාරුග හා පාලම සංවර්ධනය කිරීම හා නැඩත්තු කිරීම. පවතින මහාමාරුග පද්ධතිය වැඩි දියුණු කිරීමේ අරමුණින් නව මහාමාරුග, පාලම හා අධිවේශී මාරුග යැලපුම කිරීම, නිර්මාණය කිරීම හා ඉදි කිරීම. අනාගත ගමනාගමන හා ප්‍රවාහන ඉල්ලුම පූරෝක්තිය කිරීම තුළින් අනාගත මාරුග පද්ධති යැලපුම කිරීම හා එකී ඉල්ලුම සපුරාලීම සඳහා අවශ්‍ය ව්‍යාපෘති යෝජනා සැකසීම. ගමනාගමනය හා ආරක්ෂාව පිළිබඳ සාමාජික අභිලාෂයන් තහවුරු කළ හැකි පරිදි මාරුග පද්ධතිය ඉදි කිරීම හා සංවර්ධනය කිරීම. සම්මත පිරිවනරයන්ට අනුකූලව මාරුග පද්ධති ඉදි කිරීම හා නැඩත්තු කිරීම තුළින් මහජනයාගේ ප්‍රවාහන අවශ්‍යතා වලට බාධාකාරී නොවන ආකාරයේ මාරුග පද්ධතියක් ඇති කිරීම. මහජන මූදල් වැය කරමින් ඉදි කරන මාරුග පද්ධති තුළින් ප්‍රමාණවත් ආරක්ෂා ප්‍රතිලාභ නැවත මහජනයා වෙතවම ලැබෙන බව තහවුරු කිරීම සඳහා අදාළ ව්‍යාපෘති වලට අදාළව ගක්‍යනා අධ්‍යයන කටයුතු සිදු කිරීම හා අදාළ ව්‍යාපෘති පිළිබඳ පැවැත්‍ර අගය කිරීම සිදු කිරීම.
රාජ්‍ය සංවර්ධන හා නිර්මාණ නීතිගත සංස්ථාව		<ul style="list-style-type: none"> මාරුග, පාලම, ගොඩනැගිලි, ජල සම්පාදන ව්‍යාපෘති, වැව ප්‍රතිසංස්කරණය, පෙර සිව් කොන්ත්‍රීට නිපැයුම හා ඉදිකිරීම අමුදව්‍ය නිෂ්පාදනය කිරීම

Ministry of Highways - Organization Structure

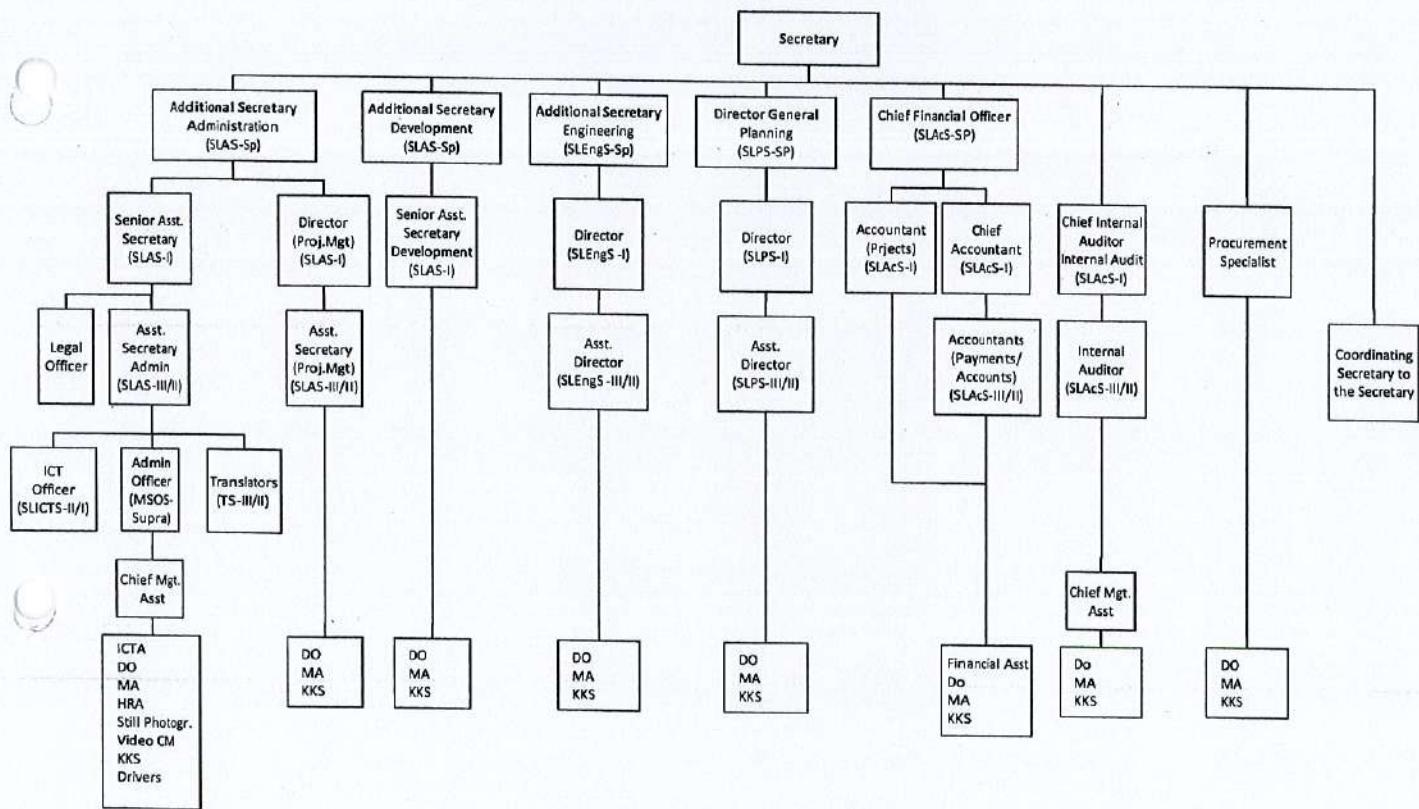

1.1 සංවිධාන සටහන

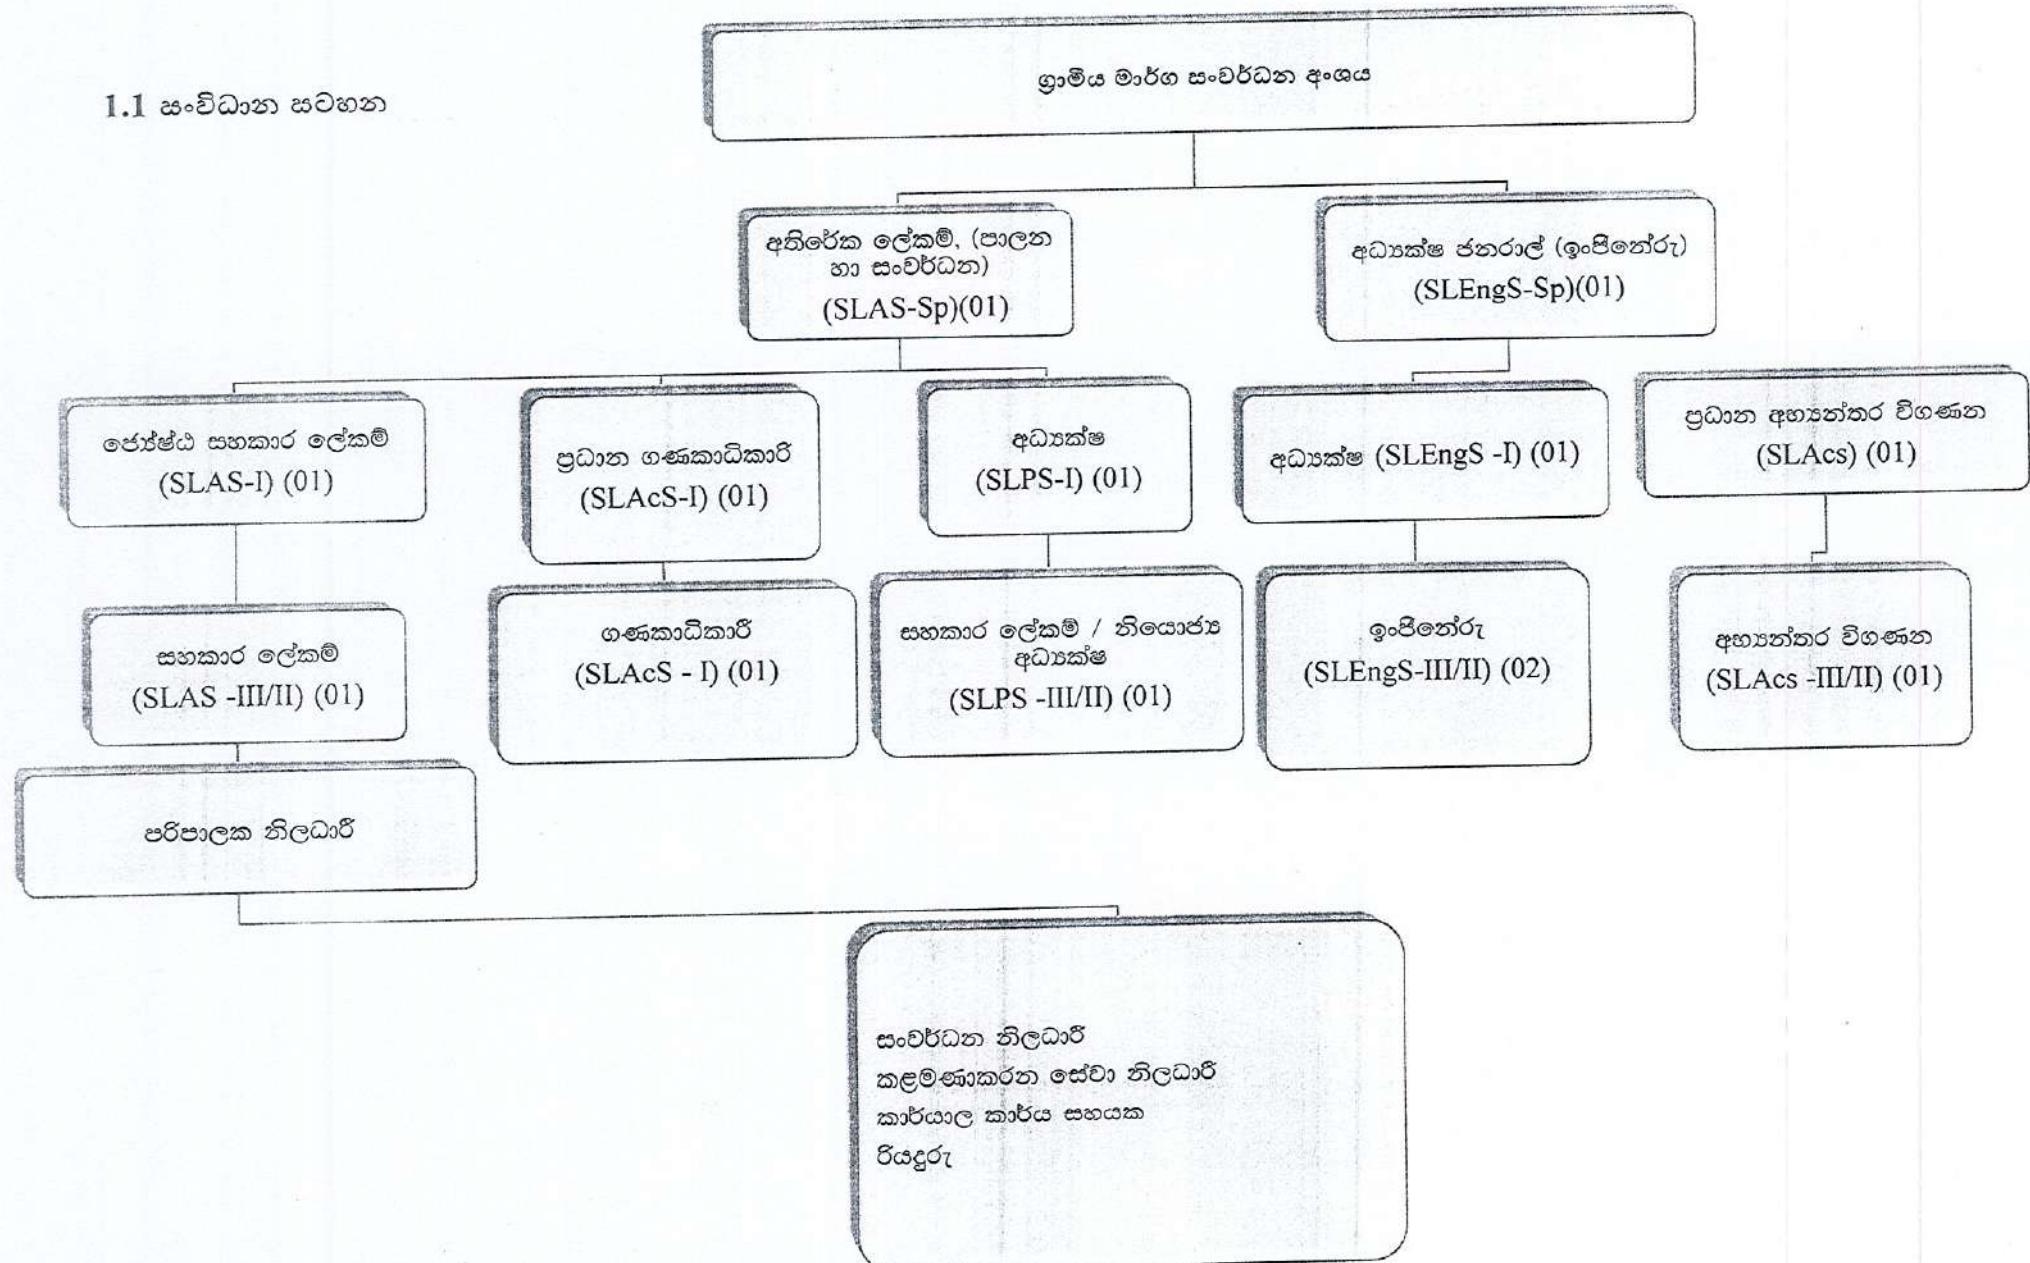

සිර්සය - 117 මහාමාරිය අමාත්‍යාංශය

01-මෙහෙයුම වැඩසටහන

01-ಅಮಾನ್ಯ ಕಾರ್ಯಾಲಯ

(5)

යිරිය	වැඩපත	ව්‍යාපෘති	කාණ්ඩා	පිටුව	පිටුව	අයිතම විස්තරය	2022.06.30 -	2022.06.30 -	ප්‍රතිපාදන ඉතිරිය	% ව්‍යුහ
							31.12.2022 දිනට ඇද්ධ ප්‍රතිපාදන	31.12.2022 දිනට ඇද්ධ වියදම		
පුනරුවරූපන වියදම							33,571,548	26,597,749.14	6,973,798.87	79
						පුද්ගල පේනයි	9,660,270	8,298,761.02	1,361,509.38	86
117	1	1	1001		11	වැටුප් හා ලේනන	5,926,811	5,739,310.08	187,500.42	97
117	1	1	1002		11	අතිකාල හා තීව්‍ය දින දීමනා	1,032,102	519,811.00	512,291.49	50
117	1	1	1003		11	අනෙකුත් දීමනා	2,701,357	2,039,639.94	661,717.47	76
						යමන් වියදම්	790,476	246,566.00	543,910.00	31
117	1	1	1101		11	දේශීය	790,476	246,566.00	543,910.00	31
117	1	1	1102		11	විදේශීය	-	-	-	-
						සුපළම්	13,133,735	12,993,012.79	140,721.93	99
117	1	1	1201		11	ලිපිද්‍රව්‍ය හා කාර්යාලයීය අවශ්‍යතා	718,900	642,633.07	76,266.93	89
117	1	1	1202		11	ඉන්ධන	12,218,079	12,218,078.72	-	100
117	1	1	1203		11	ආහාර පාන හා තිල ඇඳම්	196,756	132,301.00	64,455.00	67
						නඩත්තු වියදම්	8,362,395	3,629,815.27	4,732,579.46	43
117	1	1	1301		11	වාහන	8,164,727	3,498,955.15	4,665,772.19	43
117	1	1	1302		11	යන්ත්‍ර සහ යන්ත්‍රෝපකරණ	121,667	99,900.12	21,767.27	82
117	1	1	1303		11	ගොඩනැගිලි ඉදිකිරීම්	76,000	30,960.00	45,040.00	-
						සේවා	1,198,266	1,003,534.59	194,731.39	84
117	1	1	1402		11	තැපැල් හා සන්නිවේදනය	860,126	669,614.59	190,511.39	78
117	1	1	1403		11	විදුලිය සහ එලය	42,250	41,470.00	780.00	98
117	1	1	1409		11	වෙනත්	295,890	292,450.00	3,440.00	99
						මාරුකිරීම්	426,406	426,059.47	346.71	100
117	1	1	1502		11	විශාලික ප්‍රතිලාභ	426,406	426,059.47	346.71	100
මූලධන වියදම්							6,638,256	4,933,877.28	1,704,379.00	74
						මූලධන විෂකම් පුනරුත්ථාපනය හා වැඩි දියුණු කිරීම	6,338,256	4,933,877.28	1,404,379.00	78
117	1	1	2001		11	ගොඩනැගිලි සහ ඉදිකිරීම්	100,000	-	100,000.00	-
117	1	1	2002		11	යන්ත්‍ර සහ යන්ත්‍රෝපකරණ	100,000	-	100,000.00	-
117	1	1	2003		11	වාහන	6,138,256	4,933,877.28	1,204,379.00	80
						මූලධන විෂකම් අන්පත් කර ගැනීම	300,000	-	300,000.00	-
117	1	1	2102		11	ගෘහ හා ජ්‍යෙෂ්ඨ සහ කාර්යාල උපකරණ	150,000	-	150,000.00	-
117	1	1	2103		11	යන්ත්‍ර සහ උපකරණ	150,000	-	150,000.00	-
මුළු වියදම්							40,209,804	31,531,626.42	8,678,177.87	78
						11 දේශීය අරමුදල්	40,209,804	31,531,626.42	8,678,177.87	78

01-මෙහෙයුම විඛින්වතන
02-පරිපාලනය හා ආයතනික සේවා (මහාමාරිග)

(σ_L)

පි.න භාර්	විභාග	ව්‍යුහ අංශ	ව්‍යුහ අංශ	ව්‍යුහ අංශ	අයිතම විස්තරය	2022.06.30 - 31.12.2022 දිනට ඇද්ධි ප්‍රතිඵලි	2022.06.30 - 31.12.2022 දිනට ඇද්ධි වියදම	ප්‍රතිඵලි ඉකිලිය	% ප්‍රතිඵලි
					ප්‍රහරුවරකා වියදම	113,811,382	93,208,850.76	20,602,531.22	82
					පුද්ගල පැවැති	75,122,502	62,242,285.24	12,880,217.17	83
117	1	2	1001	11	වැඩිප් හා වෙනත	47,596,490	42,606,226.70	4,990,263.41	90
117	1	2	1002	11	අනිකාල හා නීතිඩු දින වැළැඳු	6,669,464	379,307.50	6,290,156.99	6
117	1	2	1003	11	අනෙකුත් දීමනා	20,856,548	19,256,751.04	1,599,796.77	92
					ගමන් වියදම	594,593	560,399.40	34,193.10	94
117	1	2	1101	11	දේශීය	38,593	35,823.00	2,769.50	93
117	1	2	1102	11	විදේශීය	556,000	524,576.40	31,423.60	94
					සැපයුම්	10,043,816	8,891,455.78	1,152,360.32	89
117	1	2	1201	11	ලිපිදුවා හා කාර්යාලයේ අවශ්‍යතා	2,021,221	2,020,637.30	584.14	100
117	1	2	1202	11	ඉන්ධන	6,709,082	6,374,733.99	334,347.55	95
117	1	2	1203	11	ආහාර පාන හා නීල ඇඳුම්	609,454	248,679.09	360,774.53	41
117	1	2	1205	11	වෙනත්	704,060	247,405.40	456,654.10	35
					නාඩික්ක වියදම	11,002,618	4,922,510.18	6,080,108.30	45
117	1	2	1301	11	වාහන	7,605,848	1,597,861.72	6,007,986.52	21
117	1	2	1302	11	යන්ත්‍ර සහ යන්ත්‍රෝපකරණ	726,770	724,648.46	2,121.78	100
117	1	2	1303	11	ගොඩනැගිලි ඉදිකිරීම	2,670,000	2,600,000.00	70,000.00	97
					සේවා	16,274,607	15,886,906.73	387,700.04	98
117	1	2	1401	11	ප්‍රවාහනය	1,924,771	1,924,450.00	321.43	100
117	1	2	1402	11	තැපැල් හා යන්ත්‍රෝපවේදනය	2,354,857	2,237,800.73	117,056.56	95
117	1	2	1403	11	ජලය සහ විද්‍යුලය	6,150,160	6,148,730.00	1,430.00	100
117	1	2	1404	11	බදුකුලී සහ පළාත් පාලන ආයතන බේදු	1,380,800	1,120,000.00	260,800.00	81
117	1	2	1409	11	වෙනත්	4,464,018	4,455,926.00	8,092.05	100
					මාරුකිරීම්	773,246	705,293.43	67,952.29	91
117	1	2	1505	11	පම්මාදම සහ දායක මූදල්	47,482	14,410.00	33,072.00	30
117	1	2	1506	11	රජයේ සේවකයින් සඳහා දේපල මාය පොලී	625,296	624,215.93	1,079.79	100
117	1	2	1703	11	රාජ්‍ය හා ප්‍රතිපත්තිය ත්‍රියාත්මක කිරීම	100,468	66,667.50	33,800.50	66
මූලධන වියදම						5,510,200.00	3,682,640.65	1,827,559.35	67
					මූලධන ව්‍යුහ අයිතම ප්‍රතිපත්තිය පාඨනය හා වැඩිදුනු කිරීම	5,256,540	3,535,906.48	1,720,633.52	67
117	1	2	2001	11	ගොඩනැගිලි සහ ඉදිකිරීම	80,000	-	80,000.00	-
117	1	2	2002	11	යන්ත්‍ර සහ යන්ත්‍රෝපකරණ	26,540	-	26,540.00	-
117	1	2	2003	11	වාහන	5,150,000	3,535,906.48	1,614,093.52	69
					මූලධන ව්‍යුහ අයිතම අත්පත් කර ගැනීම	83,660	36,250.00	47,410.00	43
117	1	2	2103	11	යන්ත්‍ර සහ යන්ත්‍රෝපකරණ	83,660	36,250.00	47,410.00	43
					හැකියා වර්ධනය	170,000	110,484.17	59,515.83	65
117	1	2	2401	11	කාර්ය මණ්ඩල ප්‍රතිපාදන	170,000	110,484.17	59,515.83	65
මුළු වියදම						119,321,582	96,891,491.41	22,430,090.57	81
					දේශීය අරමුදල්	119,321,582	96,891,491.41	22,430,090.57	81
					මුළු ව්‍යුහ අයිතම වියදම	119,321,582	96,891,491.41	22,430,090.57	81

2022.12.31 දිනට ප්‍රතිපාදන සහ වියදම

මහාමාරුග අමාත්‍යාංශය

(රු.මි)

ව්‍යාපෘතිය	වැඩකරන තු	විස්තර	2022.06.30 - 2022.12.31 දිනට ගැනීම ප්‍රතිපාදන	2022.06.30 - 2022.12.31 දිනට ගැනීම වියදම	ප්‍රතිපාදන ඉතිරිය	% පෙනීම
මුළු වියදම			168,892.82	111,739.68	57,153.14	66.16
මුළු විදේශීය වියදම			73,702.39	34,904.27	38,657.20	47.36
මුළු දේශීය වියදම			95,190.43	76,835.41	18,222.12	80.72
<hr/>						
අමාත්‍යාංශය	අමාත්‍ය කාර්යාලය					
	දේශීය		40.21	31.53	8.68	78.41
	පරිපාලනය හා ආයතනික සේවා (මහාමාරුග)					
	දේශීය		119.32	96.89	22.43	81.20
RDA	මාරුග සංවර්ධන අධිකාරිය					
	විදේශීය					
	දේශීය		79,788.04	70,857.24	8,930.80	88.81
CEP	මධ්‍යම අධිවේගී මාරුග ව්‍යාපෘතිය					
	විදේශීය		28,733.13	-	28,733.13	-
	දේශීය		7,262.06	2,416.75	4,845.31	33.28
REP	කොළඹ - රත්නපුර - පැල්මුවල අධිවේගී මාරුග ව්‍යාපෘතිය					
	විදේශීය					
	දේශීය		1,245.54	101.82	1,143.72	8.17
Elivated Highway	නැව කැළණී පාලමේ සිට අනුරුගිරිය දක්වා කැඳු මත ඉදි කෙරෙන අධිවේගී මාරුග ව්‍යාපෘතිය					
	විදේශීය					
	දේශීය		64.95	64.95	-	100.00
Port Access	කුඩා මත ඉදි කෙරෙන වරාය පිවිළුම අධිවේගී මාරුග ව්‍යාපෘතිය					
	විදේශීය		12,182.98	7,898.55	4,284.43	64.83
	දේශීය		91.50	12.17	79.33	13.30
SPMU	විශේෂ ව්‍යාපෘති කළමනාකරණ අංශය					
	විදේශීය		242.02	0.00	242.02	0.00
	දේශීය		379.77	28.34	351.43	7.46
MFAP	විවිධ විදේශාධාර ව්‍යාපෘතිය					
	විදේශීය		2,985.67	2,804.19	181.48	93.92
	දේශීය		4,864.40	2,959.47	1,904.93	60.84
HUNAN	මධ්‍යම හා උච්ච පළාත්වල මාරුග සහ පාලම් පුළුල් කිරීම හා වැඩි දියුණු කිරීම					

ව්‍යුහය	පිළිබඳ තොරතුරු	ගිණුම් විසින්	2022.06.30 - 2022.12.31 දිනට ඉදෑද ප්‍රතිඵාදන	2022.06.30 - 2022.12.31 දිනට ඉදෑද වියදම	ප්‍රතිඵාදන ඉතිරිය	% හැඳුනු තී
	විදේශීය		1,101.35	0.00	1,101.35	0.00
	දේශීය		50.73	36.83	13.90	72.60
SRCP	දක්ෂීණ මාර්ග සම්බන්ධතා ව්‍යාපෘතිය					
	විදේශීය		1,167.71	1,004.37	163.34	86.01
	දේශීය		646.92	45.76	601.16	7.07
TPPF	ප්‍රවාහන ව්‍යාපෘති සූදානම් කිරීමේ පහසුකම්					
	විදේශීය		75.00	37.14	37.86	49.52
	දේශීය		40.00	-	40.00	-
I Road	ඒකාබද්ධ මාර්ග ආයෝජන වැඩයටහන					
	විදේශීය		21,976.62	20,536.99	1,439.63	93.45
	දේශීය		146.06	11.43	134.63	7.83
BCRIP	ජේරාදෙණිය- බදුල්ල-වෙන්කලධි මාර්ගයේ - බදුල්ල පිට වෙන්කලධි දක්වා කොටස පුහුරුන්පාපනාය කිරීම					
	විදේශීය		2,107.09	530.17	1,576.92	25.16
	දේශීය		132.71	40.31	92.40	30.38
TCAMP	ප්‍රවාහන සම්බන්ධතා සහ වත්කම් කළමනාකරණ ව්‍යාපෘතිය					
	විදේශීය		236.31	197.74	38.57	83.68
	දේශීය		16.10	7.09	9.01	44.03
Kandy Tunnel	මහනුවර උමග ඉදිකිරීමේ ව්‍යාපෘතිය					
	විදේශීය		-	-	-	-
	දේශීය		30.51	23.51	7.00	77.06
SNKB	දෙවෙනි නව කුලේන් පාලම ඉදිකිරීමේ ව්‍යාපෘතිය					
	විදේශීය		674.55	624.72	49.83	92.61
	දේශීය		65.76	50.56	15.20	76.89
ICDP	අන්තර්ගතිකව සම්බන්ධීත සංවර්ධන					
	විදේශීය		1,985.97	1,252.33	733.64	63.06
	දේශීය		40.22	18.05	22.17	44.87
LDPP	ජානික මාර්ග ජාලය නායුම් ආපදා වලින් ආරක්ෂා කිරීමේ ව්‍යාපෘතිය					
	විදේශීය		75.00	-	75.00	-
	දේශීය		15.63	15.61	0.02	99.87
KMTTDP	මහනුවර බිජුරිධ ප්‍රවාහන පරියන්ත සංවර්ධන ව්‍යාපෘතිය					
	විදේශීය		159.00	18.08	140.92	11.37
	දේශීය		150.00	17.10	132.90	11.40

**REVISED PROCUREMENT
PLAN- HIGHWAY SECTION
FOR THE YEAR - 2022**

MINISTRY OF TRANSPORT & HIGHWAYS

Ministry of Transport & Highways

Summary of the Procurement Plan for the Year – 2022 for Highway Section

No.	Name of the Project	Total Estimated Cost for the Year 2022	
			Rs.mn.
1	Central Expressway Project (I, II, III, IV) I Rs.mn. 5,327.00 II Rs.mn. 148.00 III Rs.mn. 20,784.46 IV Rs.mn. 2,826.75		29,086.21
2	Port Access Elevated Highway Project (PAEHP)		9,874.00
3	Elevated Highway Project (EHP) – New KelaniBrige (NKB) to Athurugiriya		3,064.40
4	Ruwanpura Expressway Project (REP)		1,380.00
5	Badulla - Chenkaladi Road Improvement Project (BCRIP)		7,482.55
6	Southern Road Connectivity Project (SRCP)		1,777.00
7	Integrated Road Investment Programme (i-Road)		19,176.03
8	Landslide Disaster Protection Project (LDPP)		110.00
9	Kandy Tunnel Construction Project		600.00
10	World Bank Funded Transport Connectivity & Asset Management Project (TCAMP)		5,544.00
11	Special Project Management Project (SPMU)		1,253.12
12	Miscellaneous Foreign Aided Project (MFAP)		5,243.60
13	Local Bank Funded & Rural Roads Project (LBF& RRP)		92,000.00
14	Exim Bank of China (Hunan Branch) funded widening & improvement of 64.31km roads and re-construction of 13 bridges in Central & Uva provinces		500.00
15	Transport Project Preparatory Facility (TPPF)		340.00
16	World Bank Funded Inclusive Connectivity and Development Project (ICDP)		23,352.18
17	New Bridge Construction Project over Kelani River (NKBP)		1,280.00
18	Construction Division, RDA		3,250.00
19	Procurements carry out by Road Development Authority (RDA)		21,506.91

Contents

Page No.

Contents of the Procurement Plan - 2022 -----	i
Summary of the Procurement Plan - 2022 -----	ii, iii
1. Central Expressway Project (I, II, III, IV)-----	1 - 5
2. Port Access Elevated Highway Project (PAEHP)-----	6 - 6
3. Elevated Highway Project (EHP) – New KelaniBrige (NKB) to Athurugiriya-----	6 - 8
4. Ruwanpura Expressway Project (REP)-----	8 - 8
5. Badulla-Chenkaladi Road Improvement Project (BCRIP)-----	9 - 10
6. Southern Road Connectivity Project (SRCP)-----	10- 10
7. Integrated Road Investment Programme (i-Road) -----	10 - 12
8. Landslide Disaster Protection Project (LDPP)-----	12 - 12
9. Kandy Tunnel Construction Project-----	12 - 12
10. World Bank Funded Transport Connectivity & Asset Management Project (TCAMP)-----	13 - 14
11. Special Project Management Project (SPMU)-----	14 - 15
12. Miscellaneous foreign Aided Project (MFAP)-----	15 - 16
13. Local Bank Funded & Rural Roads Project (LBF&RRP) -----	16 - 16
14. Exim Bank of China (Hunan Branch) funded widening & improvement of 64.31km roads and re-construction of 13 bridges in Central & Uva provinces.-----	16 - 16
15. Transport Project Preparatory Facility (TPPF)-----	17 - 17
16. World Bank Funded Inclusive Connectivity and Development Project (ICDP)-----	17 - 20
17. New Bridge Construction Project over Kelani River (NKBP)-----	20 - 20
18. Construction Division, RDA-----	21 - 25
19. Procurement Carry out by Road Development Authority (RDA)-----	25 - 25
20. Others - - Road Maintenance Trust Fund (RMTF) - Infrastructure & Road Safety - Traffic Management - Gap Financing of the Road Development Authority's commitments - Land Acquisition of for completed and ongoing projects - Surveys, Investigations and Feasibility Studies	26 - 26



20.	Others		
	- Road Maintenance Trust Fund (RMTF)	Rs.mn. 3,000.00	
	- Infrastructure & Road Safety	Rs.mn. 50.00	
	- Traffic Management	Rs.mn. 50.00	
	- Gap Financing of the Road Development Authority's Commitments	Rs.mn. 35,500.00	43,180.00
	- Land acquisition for completed and ongoing projects	Rs.mn. 4,500.00	
	- Surveys, investigations & feasibility studies	Rs.mn. 80.00	
	Total of Ministry of Highways		Rs. Mn.270,000.00



Procurement Plan for the Year 2022

Serial No.	Procuring Entity (Department/Line/ Agency/ Ministry etc.)	Description 1	Vote Particulars 2	Procurement Category (Goods, Services, Works, Information Systems, Consultancy Services, etc.)	Estimated Cost for 2022 (RS.Mn.)	Source of Financing/ Name of the Donor	Procurement Method (ICB, LIB, NB, NCB & National Shopping etc.)	Level of Authority (CAPC, SCAPC, MPC, DPC, etc.)	Priority Status U=Urgent P=Priority N=Normal	Current Status of Procurement Preparedness activities	Scheduled date of commencement	Scheduled date of completion	Reference to Action Plan	Remarks
------------	---	---------------	--------------------	--	----------------------------------	--	---	--	--	---	--------------------------------	------------------------------	--------------------------	---------

I - I. Central Expressway Project Section - 1 (CEP - 01)

1	Road Development Authority/ Ministry of Highways	Construction of Central Expressway Project from 0+000-0+500 Km Including Kadawatha Interchange.	117-02-03-07-2506(17) 117-02-03-07-2105(17)	Works	5,120.00	Local Bank Lone /GOSL	NCB	CAPC	U	Bidding document under preparations	Oct-21	Apr-22		
2		Replacment of Government Buildings - MOH Building		Works	118.00	GOSL	NCB	PPC	P	Estimate and Drawing Completed. Bid document under preparations	Jan-22	Apr-22		
3		Replacment of Government Buildings Irrigation Quarters.		Works	6.00	GOSL	NCB	PPC	P		Jan-22	Apr-22		
4		Replacment of Government Buildings - Daraawa Cemetery		Works	27.00	GOSL	NCB	PPC	P		Jan-22	Apr-22		
5		Development of Resettlement Sites		Works	25.00	GOSL	NCB	PPC	P		Jan-22	Apr-22		
6		Hire /Lease Vehicles		Services	1.90	GOSL	NS	PPC/TEC	N	Continuations	Jan-22	Dec-22		
7		Office Maintenance		Goods	4.50	GOSL	NS	PPC/TEC	N	Continuations	Jan-22	Dec-22		
8		Purchase of Resettlement sites - Dansalwatta -Pasyala		Goods	22.60	GOSL	NCB	PPC	P	Valuation is in progress	Jan-22	Apr-22		
9		Purchase of Computer Accessories, office equipment & office furniture		Goods	2.00	GOSL	NS	PPC/TEC	N	Estimating	Jan-22	Dec-22		
Sub Total					5,327.00									

I - II. Central Expressway Project Section - 2 (CEP - 02)

10	Road Development Authority/ Ministry of Highways	PMU Expences - Infrastructure Development	117-02-03-07-2105/2506	Services	48.00	DF	SS	PPC	P		16.01.2017	15.11.2021		Project uses combination of DF & LBF for financing
11		Civil Works - Construction to Meerigama to Kurunegala & Ambepussa Link Road		Works	100.00	LBF	NCB	SCAPC	P	Awarded				
12		Consultancy for Meerigama to Kurunegala and Ambepussa Link Road		Services		LBF	SS	CACPC	P	Awarded				
Sub Total					148.00									

Serial No.	Procuring Entity (Department/Line/ Agency/ Ministry etc.)	Description 1	Vote Particulars 2	Procurement Category (Goods, Services, Works, Information Systems, Consultancy Services, etc.)	Estimated Cost for 2022 (RS.Mn.)	Source of Financing/ Name of the Donor	Procurement Method (ICB, LIB, LNB, NCB & National Shoping etc.)	Level of Authority (CAPC, SCAPC, MPC, DPC, etc.)	Priority Status U=Urgent P=Priority N=Normal	Current Status of Procurement Preparedness activities	Scheduled date of commencement	Scheduled date of completion	Reference to Action Plan	Remarks
------------	---	---------------	--------------------	--	----------------------------------	--	---	--	--	---	--------------------------------	------------------------------	--------------------------	---------

1 - III. Central Expressway Project Section - 3 (CEP - 03)

13	Road Development Authority/ Ministry of Highways	Feasibility Consultant by SMEC International	117-02-03-07-2506-3(17)	Service	60.00	GOSL	s/s	CACPC	P	Will be completed as and when required	Jul-21	Dec-22		
14		Stationary		Goods	1.40	GOSL	shoping	PPC	P		Jul-21	Dec-22		
15		Office Furniture, Equipment		Goods	0.50	GOSL	shoping	PPC	P		Jul-21	Dec-22		
16		Other Expences		Service & Goods	15.00	GOSL	Direct contract	PD LIMIT	P		Jul-21	Dec-22		
17		Economical Feasiblity Study by University of Moratuwa		Service	0.84	GOSL	Direct contract	PPC	P	Completed	Jul-21			
18		Feasibility Compilation Study		Service	2.32	GOSL	Direct contract	PPC	P	financial report be submitted	Feb-21	May-22		
19		Hydrology Study by SLRDC		Service	7.00	GOSL	DC	PPC	P	financial report be submitted	Jul-21	Mar-22		
20		USJP Env. Impact		Service	4.40	GOSL	DC	PPC	P	final payment to be submitted	Jul-21	May-22		
21	Road Development Authority/ Ministry of Highways	Geotechnical Investigation Work		Service	77.00	GOSL	LNB	CPCP	P		Jul-21	May-22		
22		Noice Modelin , Noise Mapping Survey		Service	9.00	GOSL	DC	PD	P	to be convened	Jul-21	May-22		
23		Construction of Central Expressway - Section 3 (Pothuhera to Galagedara) Package 1A (Ch. 0+840km to 1+580km)		works	639.00	GOSL	NCB	MPC	P	Awarded	Jul-21	May-22		
24		Construction of Central Expressway - Section 3 (Pothuhera to Galagedara) Package 1B (Ch. 1+580km TO CH2+400KM)		works	554.00	GOSL	NCB	MPC	P	Awarded	Jul-21	May-22		

19

Serial No.	Procuring Entity (Department/line/ Agency/Ministry etc.)	Description 1	Vote Particulars 2	Procurement Category (Goods, Services, Works, Information Systems, Consultancy Services, etc.)	Estimated Cost for 2022 (RS.Mn)	Source of Financing/ Name of the Donor	Procurement Method (ICB, LIB, INB, NCB & National Shipping etc.)	Level of Authority (CAPC, SCAPC, MPC, DPC etc.)	Priorities Status	Current Status of Procurement Preparedness Activities	Scheduled date of commencement	Scheduled date of completion	Reference to Action Plan	Remarks
25	Road Development Authority/ Ministry of Highways	Construction of Central Expressway - Section 3 (Pothuhera to Galagedara) Package 1C (Ch. CH2+400KM TO 3+090KM)	117-02-03-07-2506-3(17)	works	678.00	GOSL	NCB	MPC	P	Awarded	Jul-21	May-22		
26		Construction of Central Expressway - Section 3 (Pothuhera to Galagedara) Package 1D (Ch. CH3+090KM TO CH4+400KM)		works	2332.00	GOSL	NCB	SCAPC	P	Awarded	Jul-21	May-22		
27		Construction of Central Expressway - Section 3 (Pothuhera to Galagedara) Package 1E (Ch. CH4+400KM TO 4+920KM)		works	866.00	GOSL	NCB	MPC	P	Awarded	Jul-21	May-22		
28		Construction of Central Expressway - Section 3 (Pothuhera to Galagedara) Package 1F (Ch. 4+920KM TO CH.5+140KM)		works	875.00	GOSL	NCB	MPC	P	Awarded	Jul-21	May-22		
29		Construction of Central Expressway - Section 3 (Pothuhera to Galagedara) Package 1G (Ch. CH.5+140KM TO 5+820KM)		works	819.00	GOSL	NCB	MPC	P	Awarded	Jul-21	May-22		
30		Construction of Central Expressway - Section 3 (Pothuhera to Galagedara) Package 1H (Ch. 5+820KM TO 6+270KM)		works	756.00	GOSL	NCB	MPC	P	Awarded	Jul-21	May-22		
31		Construction of Central Expressway - Section 3 (Pothuhera to Galagedara) Package 1I (Ch. 6+270KM TO 6+900KM)		works	818.00	GOSL	NCB	MPC	P	Awarded	Jul-21	May-22		
32		Construction of Central Expressway - Section 3 (Pothuhera to Galagedara) Package 1J (Ch. 6+900KM TO 8+050KM)		works	2576.00	GOSL	NCB	SCAPC	P	Awarded	Jul-21	May-22		

Serial No.	Procuring Entity (Department/Line/ Agency/ Ministry etc.)	Description 1	Vote Particulars 2	Procurement Category (Goods, Services, Works, Information Systems, Consultancy Services etc.)	Estimated Cost for 2022 (RS.Mn.)	Source of Financing/ Name of the Donor	Procurement Method (ICB, LIBI, NCB, NCB & National Shopping etc.)	Level of Authority (GAPC, SCAPC, MPC, DPC etc.)	Priority Status (U= Urgent, P= Priority, N=Normal)	Current Status of Procurement Preparedness activities	Scheduled Date of commencement	Scheduled Date of completion	Reference to Action Plan	Remarks
33	Road Development Authority/ Ministry of Highways	Construction of Central Expressway - Section 3 (Pothuhera to Galagedara) Package 1K (Ch. 8+050KM TO 8+0850)		works	836.00	GOSL	NCB	MPC	P	Awarded	Jul-21	May-22		
34		Construction of Central Expressway - Section 3 (Pothuhera to Galagedara) Package 1L (Ch. 8+0850 TO 9+100KM)		works	542.00	GOSL	NCB	MPC	P	Awarded	Jul-21	May-22		
35		Construction of Central Expressway - Section 3 (Pothuhera to Galagedara) Package 1M (Ch. 9+100KM TO 9+900KM)		works	2525.00	GOSL	NCB	SCAPC	P	Awarded	Jul-21	May-22		
36		Construction of Central Expressway - Section 3 (Pothuhera to Galagedara) Package 1N (Ch. 9+900KM TO 11+230KM)		works	2923.00	GOSL	NCB	SCAPC	P	Awarded	Jul-21	May-22		
37		Construction of Central Expressway - Section 3 (Pothuhera to Galagedara) Package 1O (Ch. 11+230KM TO 11+480KM)		works	631.00	GOSL	NCB	MPC	P	Awarded	Jul-21	May-22		
38		Construction of Central Expressway - Section 3 (Pothuhera to Galagedara) Package 1P (Ch. 11+480KM TO 12+000KM)		works	444.00	GOSL	NCB	MPC	P	Awarded	Jul-21	May-22		
39		Construction of Central Expressway - Section 3 (Pothuhera to Galagedara) Package 1Q (Ch. 12+000KM TO 12+890KM)		works	1793.00	GOSL	NCB	SCAPC	P	Awarded	Jul-21	May-22		
40		Design, Build, Finance, Operate, Maintain and Transfer of Section from Rambukkana to Galagedara of CEP 03	117-02-03-07-2506-3(17)	works		Concessionaire, GOSL	ICB	CANC	P	Proposal is being evaluated	Jul-21	Jun-24		This will be implemented as an Investment Project

Serial No.	Procuring Entity (Department/Line/ Agency/Ministry etc.)	Description 1	Vote Particulars 2	Procurement Category (Goods, Services, Works, Information Systems, Consultancy Services, etc.)	Estimated Cost for 2022 (Rs. Crs.)	Source of Financing/ Name of the Donor	Procurement Method (ICB, LIB, NB, NCB & National Shopping etc.)	Level of Authority (CAPC, SCAPC, MPC, DPC etc.)	Priority Status (U=Urgent P=Priority N=Normal)	Current Status of Procurement Preparedness activities	Scheduled date of commencement	Scheduled date of completion	Reference to Action Plan	Remarks
------------	--	---------------	--------------------	--	------------------------------------	--	---	---	--	---	--------------------------------	------------------------------	--------------------------	---------

Sub Total

20.34.00

41	Road Development Authority/ Ministry of Highways	Construction of CEP- 4 (from Kurunegala to Dambulla)	117-02-03-7(2506)4-12	Works	300.00	Investor Financing	LIB	CANC	P	Submitted for Cabinet Approval	Dec.2021	Jan.2022		proposal of the investor is submitted to the General Treasury
42		Construction Supervision of Central Expressway Project - 4 (from Kurunegala to Dambulla)		Consultancy Service	2,500	GOSL	LIB	CACPC	P	RFP submitted and Evaluation work is in Progress	Dec.2021	Jan.2022		The procurement work is in progress

Additional studies & Investigations

43	Road Development Authority/ Ministry of Highways	Economical Feasibility Studies - University of Moratuwa	117-02-03-7(2506)4-17	works	2.35	GOSL	Direct Contract	DPC	P	Completed and Revisional work is in progress	Sep-21	Apr-22		To be prepared in several stages
44		SLLRDC		works	2.4	GOSL	Direct Contract	DPC	P					
45		Dept. of Archiological		Works	8.00	GOSL	Direct Contract	DPC	P		Oct.2021	Mar-22		
46	Road Development Authority/ Ministry of Highways	ESDD-Biological & Ecological survey	117-02-03-7(2506)4-17	Works	6.00	GOSL	NCB	DPC	P	RFP prepared and procurement work is in Progress	Nov-21	Jan.2022		
47		ESDD-Base line survey work		Works	8.00	GOSL	NCB	DPC	P	RFP submitted and Evaluation work is in Progress	Oct.2021	Dec.2021		

Sub Total

23.26.00

Cf6

Serial No.	Procuring Entity (Department/Line/ Agency/ Ministry etc.)	Description I	Vote Particulars	Procurement Category (Goods, Services, Works, Information Systems, Consultancy Services, etc.)	Estimated Cost for 2022 (Rs. Mm.)	Source of Financing/ Name of the Donor	Procurement Method (ICB & IBL NBN, NCB & National Shopping etc.)	Level of Authority (CAPC, SCAPC, MPC, DPC, etc.)	Priority Status (U-Urgent, P-Priority, N-Normal)	Current Status of Procurement Preparedness activities	Scheduled date of commencement	Scheduled date of completion	Reference to Action Plan	Remarks
------------	---	---------------	------------------	--	-----------------------------------	--	--	--	--	---	--------------------------------	------------------------------	--------------------------	---------

48	Road Development Authority/ Ministry of Highways	Installation of ETC System	117-02-03-16-2506-12	Works	574.00	ADB	ICB	SCAPC	P	Awarded	Feb-22	Feb-25		
49		Supervision Consultant for ETC System		Consultancy Services	500.00	ADB	ICB	MPC	P	Consultant has been identified	Feb-20	Feb-25		
50		Ramps 1 & 2 & Connecting roads		Works	7,500.00	ADB	NCB	SCAPC	U	TEC will be appointed	Apr-22	May-25		
51		Construction of Maritime Facilitation Centre for Sri Lanka Ports Authority		Works	1,300.00	ADB	NCB	SCAPC	P	Awarded				

Sri Lanka Land Reclamation and Development Authority										NKB to Rajagiriya (Phase I)				
52		Resettlement	15-2105-11	Goods	480.00	GOSL	Direct Contracting	CAPC	P	MOU is signed with UDA	Jan-20	Feb-22		Land Land Impairment
53	Road Development Authority/	Utility Shifting	15-2506-11	Service	192.60	GOSL	Direct Contracting	CAPC	U	MOU is in progress	Jan-22	Dec-23		Infrastructure Development

15

Serial No.	Procuring Entity (Department/Line/ Agency/ Ministry etc.)	Description	Vote Particulars	Procurement Category (Goods, Services, Works, Information Systems, Consultancy Services, etc.)	Estimated Cost for 2022 (Rs. Mn.)	Source of Financing	Procurement Method (ICB, LIBL, NB, NCB & National Shopping etc.)	Level of Authority (CAPC, SCAPC, MPC, DPC etc.)	Priority Status (U=Urgent, P=Priority, N=Normal)	Current Status of Procurement Preparedness activities	Scheduled date of commencement	Scheduled date of completion	Reference to Action Plan	Remarks
54	Ministry of Highways	Indipendant Engineer	funded by the Investor	Consultancy	1,000.00	Concessioner	ICB	CPCC	U	Evaluation of EOI is in process	Oct-21	Dec-24		Foreign Direct Investment (FDI)
Rajagiriya to Athurugiriya (Phase II)														
55	Road Development Authority/ Ministry of Highways	EIA , Hydrology report from SLLRDC and Noise modal	15-2506-11	Consultancy	32.40	GOSL	LNB/ variation	CPCM	U	Evaluation in Progress	Oct-21	May-22		Infrastructure Development
56	Road Development Authority/ Ministry of Highways	Utility Shifting	15-2506-11	Service	1,307.40	GOSL	Direct Contracting	CAPC	U	Estimating is in progress	Jun-22	Dec-23		
PMU Cost														
57	Road Development Authority/ Ministry of Highways	Purchase of office equipment and furniture	15-2506-11	Goods	6.98	GOSL	Shopping	PPC	P	Items and quantities identified	Jan-22	Dec-22		
58		Purchase of stationaries	15-2506-11	Goods	1.20	GOSL	Shopping	PD	N	Items and quantities identified	Jan-22	Dec-22		
59		Vehicle Rent	15-2506-11	Service	32.52	GOSL	Shopping	PPC	N	Budgeted for 2022	Jan-22	Dec-22		
60		Building Rent	15-2506-11	Service	3.96	GOSL	Shopping	PPC	N	Budgeted for 2022	Jan-22	Dec-22		
61		Security Service	15-2506-11	Service	0.96	GOSL	Shopping	PPC	N	Budgeted for 2022	Jan-22	Dec-22		PMU Cost

Serial No.	Procuring Entity (Department/Panel/ Agency/Ministry etc.)	Description 1	Vote Particulars 2	Procurement Category (Goods/ Services/ Works/ Information Systems/ Consultancy Services, etc.)	Estimated Cost for 2022 (RS. Min.)	Source of Financing/ Name of the Donor	Procurement Method (JCB/JBL/NB/NCB & National Shopping etc.)	Level of Authority (GAPC/ SCAPC/ MPC/ DPC etc.)	Priority Status (U=Urgent/ P=Priority/ N=Normal)	Current Status of Procurement (Preparation/ Activation)	Scheduled Date of Commencement	Scheduled Date of Completion	Reference No. to Action Plan	Remarks
62	Road Development Authority/ Ministry of Highways	Janitorial Services	15-2506-11	Service	0.82	GOSL	Shopping	PPC	N	Budgeted for 2022	Jan-22	Dec-22		
63		Repair & Maintenance of Vehicle	15-2506-11	Works	0.60	GOSL	Shopping	PD	N	Budgeted for 2022	Jan-22	Dec-22		
64		Repair & Maintenance of Office Equipment	15-2506-11	Works	0.40	GOSL	Shopping	PD	N	Budgeted for 2022	Jan-22	Dec-22		
65		Electricity & Water	15-2506-11	Service	1.56	GOSL	Direct Contracting	PD	N	Budgeted for 2022	Jan-22	Dec-22		
66		Telephone	15-2506-11	Service	1.50	GOSL	Direct Contracting	PD	N	Budgeted for 2022	Jan-22	Dec-22		
67		Fuel	15-2506-11	Goods	1.50	GOSL	Shopping	PD	N	Budgeted for 2022	Jan-22	Dec-22		
68	Road Development Authority/ Ministry of Highways	Land Improvements & Infrastructure Development	117-02-03-13-2105-11/ 117-02-03-13-2506-11	Works/ Services	1,380.00	GOSL	NCB	SCAPC	N	Awarded				

Serial No.	Procuring Entity (Department/Line/ Agency/ Ministry etc.)	Description 1	Vote Particulars	Procurement Category (Goods, Services, Works, Information Systems, Consultancy Services, etc.)	Estimated Cost for 2022 (Rs. Mn.)	Source of Financing/ Name of the Donor	Procurement Method (ICB, L1B1, NBN, NCB & National Shopping etc.)	Level of Authority (CAPC, SCAPC, MPC, DPC etc.)	Priority Status (U=Urgent, P=Priority, N=Normal)	Current Status of Procurement Preparedness activities	Scheduled date of commencement	Scheduled date of completion	Reference to Action Plan	Remarks
69	Road Development Authority/ Ministry of Highways	improvements to PBC road (A05) - Balance work from Lunugala to Bibile / OFID-03B (171+800km - 180+500km)	117-2-4-41-2506-12	Works	1,341.94	OFID	NCB	MPC	P	Submitted Bidding documents to Donor's Concurrence	Dec. 2021	Dec. 2022	When the donor's concurrence for bidding document's received, Paper advertisements will be published.	
70		Improvements to PBC road (A05)- Balance work from Lunugala to Bibile / OFID-03C (180+500km - 190+800km)			1,136.31									
71		Improvements to CRWB road (A004) from Beragala to Wellawaya Section (194+000 km – 207+000 km) - OFID/04			1,504.30									
72	Road Development Authority/ Ministry of Highways	Improvements to Ampara Uhana Mahoya road (A27) Section from 33+000km to 45+000 km-SFD/04A	117-2-4-23-2506-12	Works	1,122.68	SFD	NCB	MPC	P	Preparing Engineer's Estimates and Bidding documents	Feb. 2022	May 2023	When the donor's concurrence for new proposals received, procurement process can proceed.	
73		Improvements to Ampara Uhana Mahoya road (A27) Section from 45+000km to 57+780 km -SPD/04B			1,029.33									
74		Reconstruction of Bridge no.241/1 across Mahaoya in PBC road (A05) - SFD/05			758.52									

Serial No	Procuring Entity (Department/Line Agency/Ministry etc.)	Description	Vote Particulars	Procurement Category (Goods, Services, Works, Information Systems, Consultancy Services, etc.)	Estimated Cost for 2022 (RS.Mrs)	Source of Financing	Name of the Donor	Procurement Method (ICB, IIBI, NRNCB & National Shipping etc.)	Level of Authority (CAPC, SCAPC, MPC, DRC etc.)	Priority (U=Urgent, P=Pending, N=Normal)	Current Status of Procurement Preparation Activities	Scheduled Date of Completion	Reference No.	Action Plan	Remarks	
Sub Total	Grand Total															
75		Roads for 100,000km program			589.47								April-22			This implementation awaiting further contract
76	Road Development Authority/Ministry of Highways	Selected Sections of Pamankada - Horana & Kirulapone - Godagama Road (RDA/SRPCP/ICB/ADB/CP 05)	117-2-4-43 - 2506-12	Works	1,777.00	ADB	ICB	CAPC	P	Already Prepared	Commenced	30.06.2022			This is an ongoing project going under SRCP project be done mid next	
77	Road Development Authority/Ministry of	Peliyagoda - Puttalam Road (A003) from 89+000 km to 126+800 km (RMC/06/E, F, G, H)	Road Development Authority/Mi	Works	900.00					Bidding Document / MPC, ADB approval	NCB	MPC	P	21.11.21	21.03.22	
78				Works	1,136.03						NCB	MPC	P	21.11.21	21.03.22	
79				Works	1,300.00						NCB	MPC	P	21.11.21	21.03.22	
80				Works	1,000.00						NCB	MPC	P	21.11.21	21.03.22	

Serial No.	Procuring Entity (Department/Line Agency/Ministry etc.)	Description 1	Vote Particulars 2	Procurement Category (Goods, Services, Works, Information Systems, Consultancy, Services, etc.)	Estimated Cost for 2022 (RS.Mn.)	Source of Financing/Name of the Donor	Procurement Method (ICB/LIBL/NB/NCB & National Shopping etc.)	Level of Authority (CAPC/SCAPC etc.)	Priority Status (U=Urgent P=Priority N=Normal)	Current Status of Preparedness Activities	Scheduled date of commencement	Scheduled date of completion	Reference to Action Plan	Remarks	
											Scheduled date of commencement	Scheduled date of completion	Reference to Action Plan		
81	Highways Road Development Authority/ Ministry of Highways	Awissawella - Hatton - Nuwara Eliya (A007) Road (RMC08 A, B)	Ministry of Highways Road Development Authority/Ministry of Highways	Works	1,250.00	ADB	NCB	MPC	P	Preparation of due diligence	21.11.21	15.04.22			
82				Works	1,150.00		NCB	MPC	P		21.11.21	15.04.22			
83		Balangoda - Bowatte - Kaltota (B038) Road (RMC/09/A, RMC/09/B)		Works	800.00		NCB	MPC	P		21.11.21	15.04.22			
84				Works	900.00		NCB	MPC	P		21.11.21	15.04.22			
85		Dikwella - Beliatte (B101) Road (RMC/09/B)		Works	900.00		NCB	MPC	P		21.11.21	15.05.22			
86		Weerawila - Tissa - Kataragama (B464) Road (RMC/09/B)		Works	1,200.00		NCB	MPC			21.11.21	15.05.22			
87		Tawalama - Neluwa - Batuwangala (B411) Road (RMC/09/B)		Works	650.00		NCB	MPC			21.11.21	15.05.22			
88	Road Development Authority/ Ministry of Highways	Rehabilitation and Maintenance of Rural Roads in North Western Province - (KU3R, KU4R1, KU4R2, KU4R3, KU5R, PU2R1, PU2R2 & PU3R)	Road Development Authority/Ministry of Highways	Works	1,200.00	ADB	NCB	MPC		Procurement process is completed. 2022 allocation is included.					
89		Rehabilitation, Improvements of Rural Roads in the Kalutara District (KL3R1-R3)		Works	1,000.00		NCB	MPC							
90		Colombo - Kandy Road (A001) from 44+300km to 100+000km / RMC 01		Works	1,500.00		NCB	MPC							
91		Thalawa - Kekirawa - Ganewalpola - Dachchihalmilwa Road (Six Contract Packages) / RMC 05		Works	2,500.00		NCB	SCAPC							

CRS

Serial No.	Procuring Entity (Department/Line/ Agency/Ministry etc.)	Description 1	Vote Particulars 2	Procurement Category (Goods, Services, Works, Information Systems, Consultancy Services, etc.)	Estimated Cost for 2022 (Rs. Mm)	Source of Financing Name of the Donor	Procurement Method (ICB/LIBL/NB/NCB & National Shopping etc.)	Level of Authority (CAPC, SCAPC, MPC, DFC etc.)	Priority Status (U=Urgent, P=Priority, N=Normal, F=Future)	Current Status of Procurement Preparedness activities	Scheduled date of commencement	Scheduled date of completion	Reference No. to Action Plan	Remarks
92		Consultancy Services for Project Implementation		Consultancy Services	1,410.00			CACPC,						
93		Project Administration & Implementation		Goods/Servises	380.00									
		Sub Total:			1,790.00									
94	Road Development Authority/ Ministry of Highways	Mitigation of Landslide	117-02-07-13-2506(12)	Consultancy Services	110.00	JICA	ICB	SCAPC	U	RFP	January 2022	December 2028		
		Sub Total:			110.00									
95	Road Development Authority/ Ministry of Highways	Consulting Services for details design,procurement support and Supervision of contract	117-2-04-054-2506(11)	Consulting Service	600.00	EDCF	ICB	SCAPC	P	RFP	January 2022	Octo. 2027		Shortlisted consultant for the project preparation of RFP compl.
		Sub Total:			600.00									

Serial No.	Procuring Entity (Department/Line Agency/Ministry etc.)	Description 1	Vote Particulars 2	Procurement Category (Goods, Services, Works, Information Systems, Consultancy Services, etc.)	Estimated Cost for 2022 (RS.Mn.)	Source of Financing/ Name of the Donor	Procurement Method (ICB/LIBL NB, NCB & National Shopping etc.)	Level of Authority (CAPC, SCAPC, MPC, DPC etc.)	Priority Status S= Urgent P= Priority N= Normal	Current Status of Procurement Preparedness activities	Scheduled date of commencement	Scheduled date of completion	Reference to Action Plan	Remarks
96	Road Development Authority/Ministry of Highway s	Value Engineering and Introduction of Climate Resilience Strategies for National and Provincial Roads in Sri Lanka	117-2-4-48-2506 (12)	Consultancy Services	115.00	World Bank	ICB	CPCM	P	RFP Issued.	Sep-20	Feb-22		
97		Preparation of Asset Inventory and Valuation of Assets in Road Development Authority		Consultancy Services	95.00	World Bank	ICB	CPCM	P	Awaiting WB NOC for RFP Document.	Oct-20	Feb-22		
98		Consultancy service for HIMS/HDM4		Consultancy Services	15.00	World Bank	ICB	CPCM	N	Preperation TOR inprogress	May-22	Aug-22		
99		Preparation of Asset Inventory and Condition Survey of Assets in Road Development Authority		Non-consultancy Services	50.00	World Bank	NCB	PPC	P	Preperation of Employer Requirement (TOR) inprogress	Nov-21	Feb-22		
100		Enhancement of SLRAMS for inclusion of existing drainage structure information (culverts side drains) module by providing data collection mobile/ tap App.		Non-consultancy Services	50.00	World Bank	DC	PPC	P	Proposal Evaluation Inprogress	Oct-21	Jan-22		
101		Procurement of 01 No. ArcGIS Server, 4 nos HDM 4 for TCAMP & RDA		Goods	18.00	World Bank	Shopping & DC	PPC	N	Preperation specification inprogress	Feb-22	May-22		
102		Procurement of Traffic Survey Instruments for Road Development Authority.	117-2-4-48-2506 (12)	Goods	60.00	World Bank	ICB	PPC	P	Awaiting TEC recommendation for Bidding Document	Aug-21	Mar-22		

CRS

Serial No.	Procuring Entity (Department/Line/ Agency/ Ministry etc.)	Description 1	Vote Particulars 2	Procurement Category (Goods, Services, Works, Information Systems, Consultancy Services, etc.)	Estimated Cost for 2022 (RS Mn.)	Source of Financing/ Name of the Donor	Procurement Method (ICE/LIBI/NB/NCB & National Shopping etc.)	Level of Authority (CAPC, SCAPC, MRC, DPC etc.)	Priority (U=Urgent, P=Priority, N=Normal)	Current Status of Procurement Preparedness activities	Scheduled date of commencement	Scheduled date of completion	Reference to Action Plan	Remarks
103	Road Authority/Ministry of Highways	Procurement of One Unit Road Milling Machine for Road Development Authority	117-2-6-25-2506(12)	Goods	125.00	World Bank	ICB	PPC	P	Awaiting TEC recommendation for Bidding Document	Aug-21	Feb-22		
104		Procurement of Walking Profiler			10.00	World Bank	NCB	PPC	N	Preparation specification inprogress				
105		Purchasing of Equipment for PMU(Laptop Computers, Air Conditioners, Photocopier, Printers)			6.00	World Bank	Shopping	PPC	N	Preparation specification inprogress	Dec-21	Mar-22		
106		Turnkey Contract for Construction of bridge and approaches across kokilai lagoon on Mulathiv - kokolai - Pulmudai Road		Works	5000.00	ceskoslovenska Obchodni bank of Czech Republic &	Un solicited	SCAPC	P	Cabinet approval obtained for Award	Feb-22	Jul-22		still no signed loan agreement
107	Road Development Authority/Ministry of Highways	Construction of Bridge no.52/1 on Colombo - Galle - Hambantota - Wellawaya Road (A002)	117-02-06-17-2506 (12)	Works	373.67	Kuwait Fund for Arab Economic Development (KFAED)	NCB	MPC	P	Status of BD-Tender documents issued	25.02.2021	15.12.2021		
108		Construction of Bridge no. 25/1 on Negombo - Giriulla Road		Works	128.46		NCB	PPC	P	Status of BD - TEC approved. Awaiting PPC approval	25.10.2021	28.03.2022		
109		Construction of Bridge no. 4/I on Ekala - Kotadeniyawa Road (B111) & Bridge no. 30/I on Kelaniya - Mudungoda Road (B214)		Works	145.79	Kuwait Fund for Arab Economic Development (KFAED)	NCB	PPC	U	Status of BD- Under evaluation by TEC	25.10.2021	31.01.2022		

Serial No.	Procuring Entity (Department/Line/ Agency/ Ministry etc.)	Description 1	Vote Particulars 2	Procurement Category (Goods, Services, Works, Information Systems, Consultancy Services, etc.)	Estimated Cost for 2022 (Rs.Mn.)	Source of Financing/ Name of the Donor	Procurement Method (ICB/LIBL NB.NCB & National Shoping etc.)	Level of Authority (CAPC SCAPC MPC, DPC etc.)	Priori ty S Status U=Ur gent P=Pr iority N=N orma l	Current Status of Procurement Preparedness activities	Scheduled date of commencement	Scheduled date of completion	Reference to Action Plan	Remarks
110		Road extension Kirulapana Junction to Dutugemunu street (Colombo - Horana road) - 0.86km	117-02-04-10-2506 (11)	Works	605.20	GOSL	NCB	MPC	P	Status of BD - Tender documents issued	28.06.2021	15.01.2022		Construction of Underpass & Single cell bridge in Baseline road

12. Miscellaneous Foreign Aided Projects (M.F.A.P)

111	Road Development Authority/ Ministry of Highways	Rehabilitation /Improvements to Piliyandala - Maharagama Road (B367) (RDA/MFAP/ICB/OFID-2/05)	117-2-4-32-2506(12) / 117-2-4-32-2506(17) / 117-2-4-32-2105(17)	Works	820.00	OPEC Fund for International Development (OFID)	ICB	SCAPC	P	Preparation of Bid document is in progress	1/3/2022	30/06/2023		There is a delay on land acquisition more than the anticipated
112		Rehabilitation /Improvements to (B 452) Walgama -Diyagama Road (RDA/MFAP/ICB/OFID-2/04)			823.60		ICB	SCAPC	N		1/3/2021	30/09/2022		
113		Widening &Improvements to Galle - Deniyaya - Madampe Road section from Sooriyakanda (Ch.86+700 km) to Rakwana (Ch. 112.6-000 km) Stage I	117-2-4-54-2506(12) / 117-2-4-54-2506(17) / 117-2-4-54-		900.00	OFID	ICB	SCAPC	P	Feasibility studies and survey works on going	2022 March	2023 March		

Serial No.	Procuring Entity (Department/Line/ Agency/ Ministry etc.)	Description	Vote Particulars 1-2	Procurement Category (Goods, Services, Works, Information Systems, Consultancy Services, etc.)	Estimated Cost for 2022 (Rs.Mn.)	Source of Financing/ Name of the Donor	Procurement Method (GCB, LIRU, NB, NCT & National Shopping etc.)	Level of Authority (CAPC, SCAPC, MPC, DPC etc.)	Priority Status (U=Urgent P=Priority N=Normal)	Current Status of Procurement Preparedness Activities	Scheduled date of commencement	Scheduled date of completion	Reference to Action Plan	Remarks
114		Construction of Flyovers over the railway line at uththarananda Mawatha and near the Slave Island Railway station	117-2-04-57-2506-17 2105(17)		2,700.00	GOSL	NCB	SCAPC	P	Awarded	2023 March	2024 March		
Sub Total:														
115	Road Development Authority/ Ministry of Highways	Rehabilitation/ Improvement of Roads under the Implementation of 100,000 Km Alternative Road System under the Government's Policy Statement of "Vistas of Prosperity and Splendor"	117-2-04-57-2506-17	Works	72,000.00	GOSL & Local Banks of Sri Lanka	NCB	MPC	Priority	Procurement work is ongoing	01.01.2022	31.12.2022		This is a 05 years programm & Procurement is carried out on phase out basis
Sub Total:														
116	Road Development Authority/ Ministry of Highways	Infrastructure Development	117-2-04-45-2506-12	Works	500.00	Exim Bank of China	NCB	PPC		2022 allocation is included				

Serial No.	Procuring Entity (Department/Line/ Agency/ Ministry etc.)	Description 1	Vote Particulars 2	Procurement Category (Goods, Services, Works, Information Systems, Consultancy Services, etc.)	Estimated Cost for 2022 (RS.Mn.)	Source of Financing	Procurement Method (ICB, LIBL, NB, NCB & National Shopping etc.)	Level of Authority (CAPC, SCAPC, MPC, DPC etc.)	Priority Status U-Urgent P-Priority N=Normal	Current Status of Procurement Preparedness activities	Scheduled date of commencement	Scheduled date of completion	Reference to Action Plan	Remarks
		Sub Total			500.00									
117	Road Development Authority/ Ministry of Highways	Infrastructure Development	117-2-04-47-2506-12	Works	340.00	ADB	ICB			2022 allocation is included				
		Sub Total			340.00									
118	Road Development Authority/ Ministry of Highways	Rehabilitation/Improvement & Maintenance of 58.4Km Rural Roads in Nikawaratiya & Kuliyapitiya Electorate in Kurunegala District	117-2-04-58-2506-12	Works	1,414.00	WB	NCB	MPC	P	Preparing Bidding Document				World Bank funded US \$ 500Mn programme and Procurement will be carried out on phase out basis
119	Road Development Authority/ Ministry of Highways	Rehabilitation/Improvement & Maintenance of 50.4Km Rural Roads in Puttalam & Kurunegala Electorate in puttalam district in North Western		Works	1,592.00	WB	NCB	MPC	P	Preparing Bidding Document				
120	Road Development Authority/ Ministry of Highways	Rehabilitation/Improvement & Maintenance of 35.62Km Rural Roads in Tangalle & Beliatta Electorate in Hambantota district in Southern		Works	836.00	WB	NCB	MPC	P	Preparing Bidding Document				
121	Road Development Authority/ Ministry of Highways	Rehabilitation/Improvement & Maintenance of 46.3Km Rural Roads in Horawapathana, Anuradhapura & Madawachchiya Electorate in Anuradhapura District		Works	950.00	WB	NCB	MPC	P	Preparing Bidding Document				

Serial No.	Procuring Entity (Department/Line/ Agency/ Ministry etc.)	Description 1	Vote Particulars 2	Procurement Category (Goods, Services, Works, Information Systems, Consultancy Services, etc.)	Estimated Cost for 2022 (RS.Ms.)	Source of Financing/ Name of the Donor	Procurement Method (ICBL, LIBL, NB, NCB & National Shopping etc.)	Level of Authority (CAPC, SCAPC, MPC, DPC etc.)	Priority Status U-Urgent P=Priority N-Normal	Current Status of Procurement Preparedness activities	Scheduled date of commencement	Scheduled date of completion	Reference to Action Plan	Remarks
122	Road Development Authority/ Ministry of Highways	Rehabilitation/Improvement & Maintenance of 55.8Km Rural Roads in Galgamuwa, Hiriyala & Kurunegala Electorate in Kurunegala District ✓	117-2-04-58-2506-12	Works	1,340.00	WB	NCB	MPC	P	Preparing Bidding Document				World Bank funded US \$ 500Mn programme and Procurement will be carried out on phase out basis
123		Rehabilitation/Improvement & Maintenance of 49.3Km Rural Roads in Laggala & Dambulla Electorate in Matale District in Central Province		Works	1,200.00	WB	NCB	MPC	P	Bid issuing is in progress	Feb-22	Oct-23		
124		Rehabilitation/Improvement & Maintenance of 57.81Km Rural Roads in Kakira, Anuradhapura & Madawachchiya Electorate in Anuradhapura District		Works	1,258.00	WB	NCB	MPC	P	Preparing Bidding Document				
125		Rehabilitation/Improvement & Maintenance of 34Km Rural Roads in Siyabalanduwa & Moaraga Electorate in Monaragala District in Uva province		Works	1,072.00	WB	NCB	MPC	P	Preparing Bidding Document				
126		Rehabilitation/Improvement & Maintenance of 76.62Km Rural Roads in Embilipitiya, Pelmadulla & Ratnapura Electorate in Ratnapura District in Sabaragamuwa province		Works	2,402.60	WB	NCB	MPC	P	Bid evaluation is in progress	Jan-22	23-Jun		
127		Rehabilitation/Improvement & Maintenance of 49.8Km Rural Roads in Rattota & Dambulla Electorate in Matale District in Central province		Works	1,320.00	WB	NCB	MPC	P	Bid issuing is in progress	Feb. 2022	Oct-23		
128		Rehabilitation/Improvement & Maintenance of 19.6Km Rural Roads in Thanamalwila & Buttala Electorate in Monaragala District		Works	618.00	WB	NCB	MPC	P	Preparing Bidding Document				

Serial No.	Procuring Entity (Department/Line Agency/Ministry etc.)	Description 1	Vote Particulars 2	Procurement Category (Goods, Services, Works, Information Systems, Consultancy Services, etc.)	Estimated Cost for 2022 (Rs. Mn.)	Source of Financing/ Name of the Donor	Procurement Method (JCB/LIBL NB/NCR & National Shopping etc.)	Level of Authority (CAPC SCAPC MPC DPC etc.)	Priority Status (U=Urgent P=Priority N=Normal)	Current Status of Procurement Preparedness activities	Scheduled date of commencement	Scheduled date of completion	Reference to Action Plan	Remarks
129	Road Development Authority/ Ministry of Highways	Rehabilitation/Improvement & Maintenance of 42.7Km Rural Roads in Thissamaharama & Hambantota Electorate in Hambantota District	117-2-04-58-2506-12	Works	1,006.00	WB	NCB	MPC	P					
130		Development of Comprehensive digital tool to prioritize provincial & Rural roads, capacity Building & Reasrch on Green & cost		Consultancy Services	2,400.00	WB	QCBS	MPC	P					
131		World Bank compliance of Environmental & Social Safeguard Requirment		Consultancy Services	200.00	WB	QCBS	MPC	P					
132		Supervision Consultancy for Civil Works (1440kms in North Western Province, North Central Province, Northern Provice & Eastern Provice		Consultancy Services	2,592.00	WB	QCBS	MPC	P	TOR preparation is in progress				
133		Supervision Consultancy for Civil Works (720kms in Central Province, Uva province & Akkareipattu District		Consultancy Services	1,296.00	WB	QCBS	MPC	P					
134		Supervision Consultancy for Civil Works (883.38kms in Sabaragamuwa province, Western province & Southern Provinces		Consultancy Services	1,590.08	WB	QCBS	MPC	P					
135		Supervision Consultancy for Civil Works (Front Runner) (76.62kms in Ratnapura district in Sabaragamuwa province)		Consultancy Services	176.00	WB	QCBS	MPC	P					
136		Environmental and Social Screening of 200km rural roads in Hambantota, Monaragala and Puttalam district		Consultancy Services	15.00	WB	CQS	MPC	P	EOI Submission closed 29th Nov.21	Jan-22	22-Apr		

CRS

Serial No.	Procuring Entity (Department/Line/ Agency/ Ministry etc.)	Description 1	Vote Particulars 2	Procurement Category (Goods, Services, Works, Information Systems, Consultancy Services, etc.)	Estimated Cost for 2022 (Rs Mn.)	Source of Financing	C Method (ICB/LIBL NB/NCB & National Shopping etc.)	Authority (CAPC, SCAPC, MPC, DPC etc.)	Level of Authority	Priority Status	Current Status of Procurement Preparedness	Scheduled date of commencement	Scheduled date of completion	Reference to action Plan	Remarks
137	Road Development Authority/ Ministry of Highways	Rehabilitation/Improvement & Maintenance of 1397.27KM Rural Roads in all 9 Provinces	117-2-04-58-2506-12	Works		WB	NCB	MPC	P	Pro. Will be started year 2023					
138		Rehabilitation/Improvement & Maintenance of 1157.24KM Rural Roads in all 9 Provinces		Works		WB	NCB	MPC	P	Pro. Will be started year 2023					
139		Furnitures		Goods	8.00	WB	Shopping	PPC & PD Limits	P		Jan-22	Jan,2023			
140		Equipments		Goods	20.00	WB	Shopping	PPC & PD Limits	P		Jan-22	Jan-23			
141		Stationary		Goods	1.50	WB	Shopping	PPC & PD Limits	P		Oct-21	Nov-22			
142		Other Expenses		sevices & Goods	45.00	WB	Shopping	PD LIMIT	P		Oct-21	Nov-22			
143	Road Development Authority/ Ministry of Highways	Infrastructure Development	117-2-06-21-2506-12	Works	1,280.00	JICA	ICB	SCAPC		Awarded					Procurement Process has been completed and payment will be made
Sub Total					1,280.00										

Serial No.	Procurement Entity (Department/Line/ Agency/ Ministry etc.)	Description 1 Particulars 2	Procurement Category (Goods, Services, Works, Information Systems, Consultancy Services, etc.)	Estimated Cost for 2022 (Rs. Mn.)	Source of Financing/ Name of the Donor	Procurement Method (ICB/LIBL/NB/NCB & National Shopping etc.)	Level of Authority (CAPC, SCAPC, MPC, DPC etc.)	Prior Inv. Status (U=Urgent, P=Priority, N=Normal)	Current Status of Procurement Preparedness Activities	Scheduled date of commencement	Scheduled date of completion	Reference to Action Plan	Remarks
144	Road Development Authority/ Ministry of Highways	Colombo - Infrastructure Development	117-02-05-2506 (1)	Works	100.00	GOSL	NCB	MPC	N	Estimate Pre.	Jan-22	Dec-22	
145		Colombo - Infrastructure Development		Works	60.00	GOSL	NCB	DPC	N	Estimate Pre.	Jan-22	Dec-22	
146		Colombo - Infrastructure Development		Works	40.00	GOSL	NCB	RPC	N	Estimate Pre.	Jan-22	Dec-22	
147		Gampaha - Infrastructure Development		Works	100.00	GOSL	NCB	MPC	N	Estimate Pre.	Jan-22	Dec-22	
148		Gampaha - Infrastructure Development		Works	60.00	GOSL	NCB	DPC	N	Estimate Pre.	Jan-22	Dec-22	
149		Gampaha - Infrastructure Development		Works	40.00	GOSL	NCB	RPC	N	Estimate Pre.	Jan-22	Dec-22	
150		Kalutara - Infrastructure Development		Works	100.00	GOSL	NCB	MPC	N	Estimate Pre.	Jan-22	Dec-22	
151		Kalutara - Infrastructure Development		Works	60.00	GOSL	NCB	DPC	N	Estimate Pre.	Jan-22	Dec-22	
152		Kalutara - Infrastructure Development		Works	40.00	GOSL	NCB	RPC	N	Estimate Pre.	Jan-22	Dec-22	
153		Kandy - Infrastructure Development		Works	95.00	GOSL	NCB	MPC	N	Estimate Pre.	Jan-22	Dec-22	
154		Kandy - Infrastructure Development	117-02-05-2506 (1)	Works	57.00	GOSL	NCB	DPC	N	Estimate Pre.	Jan-22	Dec-22	
155		Kandy - Infrastructure Development		Works	38.00	GOSL	NCB	RPC	N	Estimate Pre.	Jan-22	Dec-22	
156		Matale - Infrastructure Development		Works	70.00	GOSL	NCB	MPC	N	Estimate Pre.	Jan-22	Dec-22	
157		Matale - Infrastructure Development		Works	42.00	GOSL	NCB	DPC	N	Estimate Pre.	Jan-22	Dec-22	
158		Matale - Infrastructure Development		Works	28.00	GOSL	NCB	RPC	N	Estimate Pre.	Jan-22	Dec-22	

C6

Serial No.	Procuring Entity (Department/Line Agency/Ministry etc.)	Description 1	Vote Particulars 2	Procurement Category (Goods, Services, Works, Information Systems, Consultancy Services, etc.)	Estimated Cost for 2022 (Rs. M)	Source of Financing/ Name of the Donor	Procurement Method (ICR-LIRL NB-NCB & National Shopping etc.)	Level of Authority (CAPC, SCAPC MPC, DPC etc.)	Priority Status (U=Urgent P=Priority N=Normal)	Current Status of Procurement Preparedness activities	Scheduled date of commencement	Scheduled date of completion	Reference to Action Plan	Remarks
159	Road Development Authority/ Ministry of Highways	Nuwara Eliya - Infrastructure Development	117-02-05-2506 (1)	Works	65.00	GOSL	NCB	MPC	N	Estimate Pre.	Jan-22	Dec-22		
160		Nuwara Eliya - Infrastructure Development		Works	39.00	GOSL	NCB	DPC	N	Estimate Pre.	Jan-22	Dec-22		
161		Nuwara Eliya - Infrastructure Development		Works	26.00	GOSL	NCB	RPC	N	Estimate Pre.	Jan-22	Dec-22		
162		Matara - Infrastructure Development		Works	70.00	GOSL	NCB	MPC	N	Estimate Pre.	Jan-22	Dec-22		
163		Matara - Infrastructure Development		Works	42.00	GOSL	NCB	DPC	N	Estimate Pre.	Jan-22	Dec-22		
164		Matara - Infrastructure Development		Works	28.00	GOSL	NCB	RPC	N	Estimate Pre.	Jan-22	Dec-22		
165		Galle - Infrastructure Development		Works	70.00	GOSL	NCB	MPC	N	Estimate Pre.	Jan-22	Dec-22		
166		Galle - Infrastructure Development		Works	42.00	GOSL	NCB	DPC	N	Estimate Pre.	Jan-22	Dec-22		
167		Galle - Infrastructure Development		Works	28.00	GOSL	NCB	RPC	N	Estimate Pre.	Jan-22	Dec-22		
168		Hambantota - Infrastructure Development		Works	70.00	GOSL	NCB	MPC	N	Estimate Pre.	Jan-22	Dec-22		
169		Hambantota - Infrastructure Development		Works	42.00	GOSL	NCB	DPC	N	Estimate Pre.	Jan-22	Dec-22		
170		Hambantota - Infrastructure Development		Works	28.00	GOSL	NCB	RPC	N	Estimate Pre.	Jan-22	Dec-22		
171		Jaffna - Infrastructure Development		Works	50.00	GOSL	NCB	MPC	N	Estimate Pre.	Jan-22	Dec-22		
172		Jaffna - Infrastructure Development		Works	30.00	GOSL	NCB	DPC	N	Estimate Pre.	Jan-22	Dec-22		
173		Jaffna - Infrastructure Development		Works	20.00	GOSL	NCB	RPC	N	Estimate Pre.	Jan-22	Dec-22		
174		Killinochchi - Infrastructure Development		Works	50.00	GOSL	NCB	MPC	N	Estimate Pre.	Jan-22	Dec-22		
175		Killinochchi - Infrastructure Development		Works	30.00	GOSL	NCB	DPC	N	Estimate Pre.	Jan-22	Dec-22		
176		Killinochchi - Infrastructure Development		Works	20.00	GOSL	NCB	RPC	N	Estimate Pre.	Jan-22	Dec-22		
177		Mannar - Infrastructure Development		Works	50.00	GOSL	NCB	MPC	N	Estimate Pre.	Jan-22	Dec-22		

59

Serial No.	Procuring Entity (Department/Inc/ Agency/ Ministry etc.)	Description 1	Vote Particulars 2	Procurement Category (Goods, Services, Works, Information Systems, Consultancy Services, etc.)	Estimated Cost for 2022 (Rs.Mn.)	Source of Financing/ Name of the Donor	Procurement Method (ICB/LIBL NB/NCR & National Shopping etc.)	Level of Authority (CAPC, SCAPC, MPC, DPC etc.)	Priority (U=Urgent P=Priority N=Normal)	Current Status of Procurement Preparedness activities	Scheduled date of commencement	Scheduled date of completion	Reference to Action Plan	Remarks
178	Authority/ Ministry of Highways	Mannar - Infrastructure Development	117-02-05-2506 (1)	Works	30.00	GOSL	NCB	DPC	N	Estimate Pre.	Jan-22	Dec-22		
179		Mannar - Infrastructure Development		Works	20.00	GOSL	NCB	RPC	N	Estimate Pre.	Jan-22	Dec-22		
180		Vavuniya - Infrastructure Development		Works	50.00	GOSL	NCB	MPC	N	Estimate Pre.	Jan-22	Dec-22		
181		Vavuniya - Infrastructure Development		Works	30.00	GOSL	NCB	DPC	N	Estimate Pre.	Jan-22	Dec-22		
182		Vavuniya - Infrastructure Development		Works	20.00	GOSL	NCB	RPC	N	Estimate Pre.	Jan-22	Dec-22		
183		Mulltive - Infrastructure Development		Works	50.00	GOSL	NCB	MPC	N	Estimate Pre.	Jan-22	Dec-22		
184		Mulltive - Infrastructure Development		Works	30.00	GOSL	NCB	DPC	N	Estimate Pre.	Jan-22	Dec-22		
185		Mulltive - Infrastructure Development		Works	20.00	GOSL	NCB	RPC	N	Estimate Pre.	Jan-22	Dec-22		
186		Batticaloa - Infrastructure Development		Works	50.00	GOSL	NCB	MPC	N	Estimate Pre.	Jan-22	Dec-22		
187		Batticaloa - Infrastructure Development		Works	30.00	GOSL	NCB	DPC	N	Estimate Pre.	Jan-22	Dec-22		
188		Batticaloa - Infrastructure Development		Works	20.00	GOSL	NCB	RPC	N	Estimate Pre.	Jan-22	Dec-22		
189		Ampara - Infrastructure Development		Works	50.00	GOSL	NCB	MPC	N	Estimate Pre.	Jan-22	Dec-22		
190		Ampara - Infrastructure Development		Works	30.00	GOSL	NCB	DPC	N	Estimate Pre.	Jan-22	Dec-22		
191		Ampara - Infrastructure Development		Works	20.00	GOSL	NCB	RPC	N	Estimate Pre.	Jan-22	Dec-22		
192	Road Development Authority/ Ministry of Highways	Trincomalee - Infrastructure Development	117-02-05-2506 (1)	Works	50.00	GOSL	NCB	MPC	N	Estimate Pre.	Jan-22	Dec-22		
193		Trincomalee - Infrastructure Development		Works	30.00	GOSL	NCB	DPC	N	Estimate Pre.	Jan-22	Dec-22		
194		Trincomalee - Infrastructure Development		Works	20.00	GOSL	NCB	RPC	N	Estimate Pre.	Jan-22	Dec-22		
195		Kurunegala - Infrastructure Development		Works	60.00	GOSL	NCB	MPC	N	Estimate Pre.	Jan-22	Dec-22		

CJG

58

Serial No.	Procuring Entity (Department/Line/ Agency/ Ministry etc.)	Description I	Vote Particulars 2	Procurement Category (Goods, Services, Works, Information Systems, Consultancy Services, etc.)	Estimated Cost for 2022 (RS.M.R.)	Source of Financing Name of the Donor	Procurement Method (GCR & LIBL, NE, NCB & National Shoring etc.)	Level of Authority (CAPC, SCAPC, MPC, DPC, etc.)	Priority Status (U=Urgent P=Priority N=Normal)	Current Status of Procurement Preparedness activities	Scheduled date of commencement	Scheduled date of completion	Reference no. to Action Plan	Remarks
196	Road Development Authority/ Ministry of Highways	Kurunegala - Infrastructure Development	117-02-05-2506 (1)	Works	36.00	GOSL	NCB	DPC	N	Estimate Pre.	Jan-22	Dec-22		
197		Kurunegala - Infrastructure Development		Works	24.00	GOSL	NCB	RPC	N	Estimate Pre.	Jan-22	Dec-22		
198		Puttalam - Infrastructure Development		Works	60.00	GOSL	NCB	MPC	N	Estimate Pre.	Jan-22	Dec-22		
199		Puttalam - Infrastructure Development		Works	36.00	GOSL	NCB	DPC	N	Estimate Pre.	Jan-22	Dec-22		
200		Puttalam - Infrastructure Development		Works	24.00	GOSL	NCB	RPC	N	Estimate Pre.	Jan-22	Dec-22		
201		Anuradhapura - Infrastructure Development		Works	75.00	GOSL	NCB	MPC	N	Estimate Pre.	Jan-22	Dec-22		
202		Anuradhapura - Infrastructure Development		Works	45.00	GOSL	NCB	DPC	N	Estimate Pre.	Jan-22	Dec-22		
203		Anuradhapura - Infrastructure Development		Works	30.00	GOSL	NCB	RPC	N	Estimate Pre.	Jan-22	Dec-22		
204		Pollonnaruwa - Infrastructure Development		Works	50.00	GOSL	NCB	MPC	N	Estimate Pre.	Jan-22	Dec-22		
205		Pollonnaruwa - Infrastructure Development		Works	30.00	GOSL	NCB	DPC	N	Estimate Pre.	Jan-22	Dec-22		
206		Pollonnaruwa - Infrastructure Development		Works	20.00	GOSL	NCB	RPC	N	Estimate Pre.	Jan-22	Dec-22		
207		Badulla - Infrastructure Development		Works	60.00	GOSL	NCB	MPC	N	Estimate Pre.	Jan-22	Dec-22		
208		Badulla - Infrastructure Development		Works	36.00	GOSL	NCB	DPC	N	Estimate Pre.	Jan-22	Dec-22		
209		Badulla - Infrastructure Development		Works	24.00	GOSL	NCB	RPC	N	Estimate Pre.	Jan-22	Dec-22		
210		Monaragala - Infrastructure Development		Works	60.00	GOSL	NCB	MPC	N	Estimate Pre.	Jan-22	Dec-22		
211		Monaragala - Infrastructure Development		Works	36.00	GOSL	NCB	DPC	N	Estimate Pre.	Jan-22	Dec-22		
212		Monaragala - Infrastructure Development		Works	24.00	GOSL	NCB	RPC	N	Estimate Pre.	Jan-22	Dec-22		
213		Kegalle - Infrastructure Development		Works	60.00	GOSL	NCB	MPC	N	Estimate Pre.	Jan-22	Dec-22		

Serial No.	Procuring Entity (Department/Line/ Agency/ Ministry etc.)	Description 1	Vote Particulars 2	Procurement Category (Goods, Services, Works, Information Systems, Consultancy Services, etc.)	Estimated Cost for 2022 (Rs. Mln.)	Source of Financing/ Name of the Donor	Procurement Method (ICB, LIBL, NB, NCB & National Shopping etc.)	Level of Authority (CAPC, SCAPC, MPC, DPC etc.)	Priority S=Urgent P=Priority N=Normal	Current Status of Procurement Preparedness activities	Scheduled date of commencement	Scheduled date of completion n	Reference to Action Plan	Remarks
214	Road Development Authority/ Ministry of Highways	Kegalle - Infrastructure Development	117-02-05-2506 (1)	Works	36.00	GOSL	NCB	DPC	N	Estimate Pre.	Jan-22	Dec-22		
215		Kegalle - Infrastructure Development		Works	24.00	GOSL	NCB	RPC	N	Estimate Pre.	Jan-22	Dec-22		
216		Ratnapura - Infrastructure Development		Works	60.00	GOSL	NCB	MPC	N	Estimate Pre.	Jan-22	Dec-22		
217		Ratnapura - Infrastructure Development		Works	36.00	GOSL	NCB	DPC	N	Estimate Pre.	Jan-22	Dec-22		
218		Ratnapura - Infrastructure Development		Works	24.00	GOSL	NCB	RPC	N	Estimate Pre.	Jan-22	Dec-22		
Sub Total														
219	Road Development Authority/ Ministry of Highways	Procurements carry out by Road Development Authority	2506/2201	Goods/Works and Services	21,506.91	GOSL			N		Jan-22	22-Dec		This includes all procurements are to be carried out by all divisions (Except Construction) of RDA
Sub Total														

A/S

56

Serial No.	Procuring Entity (Department/Line/ Agency/ Ministry etc.)	Description 1	Vote Particulars 2	Procurement Category (Goods, Services, Works, Information Systems, Consultancy Services, etc.)	Estimated Cost for 2022 (Rs.Mn.)	Source of Financing/ Name of the Donor	Procurement Method (ICB, LIBL, NB/NGB & National Shopping etc.)	Level of Authority (CAPC, SCAPC, MPC, DFC etc.)	Priority Status (U=Urgent P=Priority N=Normal)	Current Status of Procurement Preparedness activities	Scheduled date of commencement	Scheduled date of completion	Reference Action Plan	Remarks
220		Road Maintenance Trust Fund	2506		3,000.00									
221		Infrastructure & Road Safety	2506		50.00									
222		Traffic Management	2506		50.00									
223		Gap Financing of the Road Development Authority's Commitments	2506		35,500.00									
224		Land Acquisition for completed and on going Projects	2105		4,500.00									
225		Surveys, Investigations and Feasibility Studies	2506		80.00									

Total Revised Estimated Amount of Highways section under Ministry of Transport & Highways for the year - 2022 as per the Procurement Plan : Rs Mn. 270,000.00

Checked by :

Recommended by :

Approved by :

J.K. Nilupul S. Perera
Chief Financial Officer
Ministry of Transport & Highways
07th Floor, "Maganeguma Mahamedura"
No. 216, Devala Road, Devala Mawatha,
Colombo 10, Sri Lanka.

R.W.R. Permasiri
Secretary
Ministry of Transport & Highways
07th Floor, "Maganeguma Mahamedura"
No. 216, Devala Road, Devala Mawatha,
Colombo 10, Sri Lanka.
